

Centennial Park West Total Project Cost

Update 6.16.25

		Subtotal	\$1,000,000	\$	918,636
•	FY23/24 Construction Administration (PH3)	1.5%	\$ 250,000	\$	176,636 <mark>*</mark>
•	FY22 Construction Documents Design (PH2)	5.1%	\$ 620,000	\$	616,000
•	FY21 Conceptual Design (PH1)	1.0%	\$ 130,000	\$	126,000
A/E Design- Wight and Company (selected through RFP)			Budget 8.3%	Co	st 7.6%



^{*} Figure factors a \$10,364 reduction due to mixing station error

Construction- Reed Construction (selected through RFP)

- FY23/24 Construction (Alt. 2-Fencing, and Alt. 3 Additional Storage)
- FY23/24 Contingency Costs
 - Includes unforeseen changes, design changes, and owner changes

Budget	<u>Cost</u>
\$10,909,091	\$10,316,128.00
\$ 1,090,909*	\$ 650,248.42

Subtotal \$12,000,000** \$10,966,376.42



^{*} Contingency set aside was reduced to \$997,330

^{** \$250}K was separated out for A/E construction administration

Reed Contingency Summary

- 89 Requests for Contingency Usage
 - 26 negotiated zero cost
 - 7 credits to Village (part of below categories cost figures)
 - 14 owner changes

\$172,004.40

- Sprinkler add to field, knox box for FD, storm pipe add, additional camera location conduit, tent-tie down material, power pedestal change, fence adjustment, additional conduit to street
- 14 design changes

\$158,725.52

- 400 amp service/lights, steel, foundation wall, retainage wall, support beam for sliding door, mixing slab change
- 28 construction changes

\$319.518.50

• Electrical gear locally assembled, liming soil, \$87K of OT for critical timeline due to weather delays, reroute sewer line, some other smaller ones

Subtotal \$650,248.42*

Detailed breakdown tracker sheets in backup slides



Owner Costs	<u>Bu</u>	dget	Со	<u>st</u>
 FY23/24 Construction Owners Costs Includes construction testing, utility fees, low voltage, furniture, etc. 	\$	0	\$	267,966.00*
FY24 VIP Event June 4Includes catering, drinks, and giveaways	\$	0	\$	4,245.17
FY25 Items				
LED Screens	\$	400,000	\$	671,500.00**
 Life safety items 	\$	300,000	\$	302,300.00
 Wayfinding signs, 3 swing gates to help PD/winter shut down 	\$	55,000	\$	28,464.00
TOTAL	\$1	.3,755,000	\$1	3,159,487.59
* No Owner Costs set aside for project so taken out of Contingency	De	escope final	\$1	2,487,987.59



This cost was descoped.

Based on Board Direction, a business plan will be developed for the facility

Owner's Cost (out of Contingency) Summary

_	Construction Material Testing		¢42 6E1 00
•	Construction Material Testing		\$43,651.00
•	Utilities Fees (ComEd/Comcast)		\$ 0.00
•	Electrical Street Light fix		\$ 4,365.00
•	Damaged sprinkler fix		\$ 2,130.00
•	Furniture and Furnishings		\$ 7,279.01
•	Weight Blocks		\$ 2,573.48
•	Signage (Interior/Exterior)		\$ 2,174.20
•	Artwork/Dedication Plaque		\$ 1,205.00
•	Cameras(18), wiring, wifi		\$67,831.00
•	Network closets-Used Cultural Arts		\$ 0.00
•	Wireless devices		\$ 5,018.49
•	Power-Spider boxes for tents		\$24,971.00
•	Power and Bird deteriorate		\$26,000.00
•	North Gates		\$12,760.00
•	Update lighting programming		\$ 4,765.00
		Total	\$267,966.00



Questions?



Backup Slides



							Owner Change Order to
Approval date	Reed COR	Change Order List		(O) Owner	(D) Design	(C) Construction	9
7/26/2023		Electrical Gear-Locally assembled	С	(0) 0	(=/===:g.:	\$34,650.00	
VOID		Rammed Aggregate Piers/Rigid Inclusions	C				CO #8
9/11/2023		Credit for raceway, 400 Amp, Additional Lights	D		\$12,741.00		CO #2
10/3/2023	7	Lime Stabilization and Time Extension due to weather delays	С		V,	\$114,590.51	
10/25/2023		Soil Turning	C			\$10,214.82	
VOID	9&11	DeMucking, turning, recompacting, winter conditions	С				CO #8
VOID		Schedule Acceleration	C				CO #8
10/6/2023	12	Additional Lime	С			\$20,150.36	
10/10/2023	13&14	Credit for smaller displays, add 8 additional smoke detectors	С			\$544.00	CO #3
4/29/2024		Additional Conduits	0	\$16,191.82			CO #6
1/22/2024	16	Architect Design Change for foundation steps for utility penetrations ASI 002	D		\$18,715.91		CO #4
11/21/2023	17	Architect Design Change for retaining wall ASI 003	D		\$17,102.66		CO #4
1/19/2024		Wind Screen Extension	D		\$10,057.88		CO #4
VOID	19	Observation Report 1 Change	С			\$0.00	CO #8
1/19/2024	20	Handrail Design Changes	D		\$4,521.77		CO #4
1/19/2024		X4 Fixture Credit RDI 50	D		-\$2,000.57		CO #4
VOID	22	Overexcavation- Extra Soil on Site	С			\$0.00	CO #8
VOID	23	Stone Building Pad	С			\$0.00	CO #8
2/19/2024		Power Pedestal Breaker Change	D		\$2,254.66		CO #5
2/12/2024		Additional Handles to Bollards	D		\$999.90		CO #5
1/22/2024	26	Additional steel from IFC Drawings	D		\$27,947.32		CO #5
2/12/2024		Masonry 1.26.24 O/T Sat	С			\$2,977.48	CO #5
2/12/2024	28	Masonry 2.3.24 O/T Sat	С			\$2,339.77	CO #5
2/12/2024	29	Masonry 1 hr 2/5-2/10 and OT Sat	С			\$5,770.00	
2/26/2024	30	Fence Adjustment and additional gate	0	\$3,264.76			CO #5
12/30/2024	31	Stage Floor- Credit Marine Grade Lumber/Add Concrete	0	-\$34,532.00			CO #8
2/19/2024	32	Sewer Line- Additional structure/reroute	С			\$33,998.82	
3/18/2024	33	Underdrain for retainage wall and tie in to trench	D		\$2,480.86		CO #6
2/19/2024	34	Masonry 1 hr 2/13-2/15	0			\$947.68	CO #5
4/29/2024		Power Pedestals for Performer Trucks	0	\$17,639.46			CO #6
10/7/2024		Concrete and Electrical 2.20.24 OT Sat	0			\$8,350.45	
7/8/2024	37	Exterior Trough Changes-concrete floor and steel modifications	D		\$11,480.55		CO #7
4/24/2024		Lawn Sprinkler System	0	\$100,941.02			CO #6
3/26/2024		Island Removal	0	\$0.00			CO #6
6/27/2024	40	Tent Tie-Downs- install	0	\$4,401.15			CO #7
4/3/2024		Support Steel for backstage sliding door	D		\$20,164.65		CO #6
5/8/2024	42	Steel OT for 3.23.24	С			\$6,688.86	CO #6



Approval date	Reed COR	Change Order List		(O) Owner	(D) Design	(C) Construction	Owner Change Order to
3/26/2024		Tent Tie-Down Material Order	0	\$10,400.30	(<i>b)</i> besign	(O) Construction	CO #6
6/27/2024		Steel OT for 3.30.24	C	\$10,400.00		\$9,044.23	
5/8/2024		Steel OT for 4.6.24	C			\$7,883.66	
VOID		Curb modification	C				CO #8
5/8/2024		Steel OT for 4.13.24 & 4.14.24	C			\$9,129.52	
VOID		Temp steel plates for park station bldvd	С				CO #8
6/27/2024		Undercuts for Vendor Path	С			\$6,960.42	
7/8/2024	50	Steel OT for 4.20.24	0			\$5,943.46	
6/15/2024	51	Structural Steel for HVAC Change	С			\$9,400.11	CO #6
5/1/2024		Additional Camera Locations	0	\$8,751.60			CO #6
5/8/2024	53	Steel OT for 4.27.24	С			\$3,308.68	CO #6
6/4/2024	54	Washroom Accessory Changes	С			\$1,457.63	CO #6
6/3/2024		Fire Inspector Final Comments	С			\$5,825.01	CO #6
VOID		Ground box	С			\$0.00	CO #8
6/27/2024	57	High Early Add Mix at Apron	С			\$945.00	CO #7
5/31/2024		Sod three area	0	\$14,048.60			CO #7
10/27/2024	59	ADA Seating Demo	D		\$19,880.00		CO #8
12/30/2024	60	12" pipe and structure in front of stage	0	\$17,207.17			CO #8
12/30/2024	61	Mixing Station Slab changes	D		\$12,378.93		CO #8
6/27/2024	62	Sprinkler Pump & Electric	0	\$7,218.57			CO #7
7/8/2024		Paint insulation black	С			\$2,400.00	
8/22/2024	64	Demo three slabs to get grade right	С			\$4,242.91	CO #8
12/30/2024	65	Open Ozinga on Sunday	С			\$20,000.00	CO #8
VOID	66	Additional Raceway Top of Wall	С			\$0.00	CO #8
VOID	67	Install 100 amp sub panel in mechanical room for sprinkler system	С				CO #8
VOID		Repairs for out of sequence asphalt	С				CO #8
VOID	69	Fire Alarm Devices in Restrooms	С			\$0.00	CO #8



Approval date	Reed COR	Change Order List		(O) Owner	(D) Design	(C) Construction	Owner Change Order to Contract
6/17/2024	70	Knox Box Monitoring	0	\$1,544.69			CO #7
6/17/2024	71	Added Light Pole Receptacles	0	\$781.43			CO #7
12/13/2024	72	Electrical Aiming of Lights	С			\$0.00	CO #8
12/23/2024	73	Electrical Overtime 5/19-6/3	С			\$4,662.41	CO #8
8/22/2024	74	Event Standby Labor for Sharlen	0	\$2,924.83			CO #8
7/8/2024	75	Dock Leveler Motor Voltage	С			\$0.00	CO #8
VOID		Electrician OT 3.2.24- Duplicate	С			\$0.00	CO #8
VOID	77	Orland Park Electrical Inspection Report Changes	С			\$0.00	CO #8
VOID		North Gate	С			\$0.00	CO #8
12/30/2024		Vendor Path Power Washing	С				CO #8
8/22/2024	80	Concert Prep OT for Concrete Pour	С			\$0.00	CO #8
6/27/2024	81	Sprinkler location pipe on east side	0	\$1,221.00			CO #7
VOID		In fill the stage with concrete	С			\$0.00	CO #8
8/22/2024	83	Steel Storage	С				CO #8
8/22/2024	84	Extended General Conditions	С			\$0.00	CO #8
12/30/2024	85	Reed vs Olrand Park Site Work	С			-\$5,173.37	CO #8
12/30/2024	86	Removal of Additional Soils	С			-\$4,857.68	CO #8
8/22/2024	87	Credit for #3 wire vs #4 wire	С			-\$3,884.24	CO #8
12/30/2024	88	Lawn Hydroseeding	С			\$1,008.00	CO #8
12/30/2024	89	Additional Fence Rental	С			\$0.00	CO #8
		Sub total		\$172,004.40	\$158,725.52	\$319,518.50	
		Total					\$650,248.42



Centennial Park West

March 20, 2023










VILLAGE OF ORLAND PARK | CENTENNIAL WEST CONCERT VENUE





- STAGE AREA
- ROLLING HILLS
- WALKING PATH
- RESTROOM
- METRA
 PARKING &
 STATION
- POND
- METRA TRACKS
- CENTENNIAL PARK TO EAST



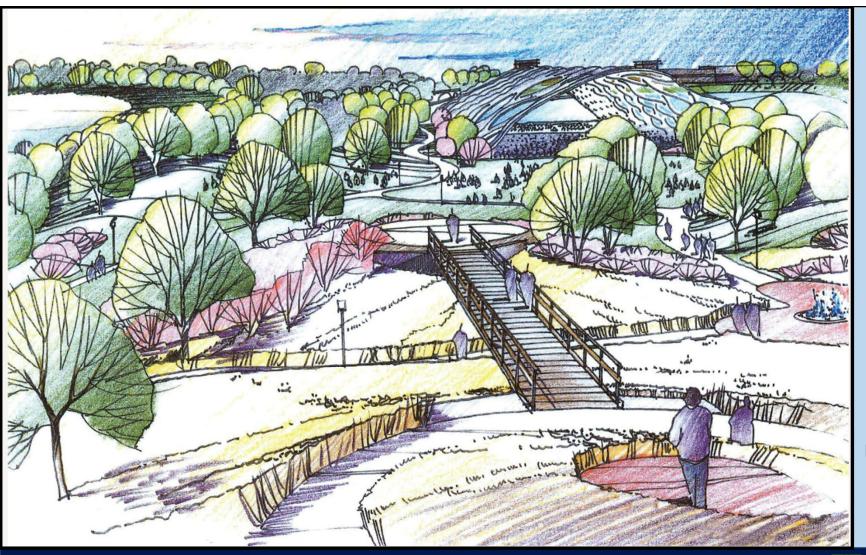

2003 COLETTE HIGHLANDS PETITION INCLUDES PLAN FOR VENUE

2005 FIRM HIRED TO COMPLETE SITE PLAN

INCLUDED

INITIAL GRADING FOR
FOUR-PHASE
LANDSCAPE PLAN
FOR THE PURPOSE OF
BUILDING AN
OUTDOOR CONCERT
VENUE FOR
COMMUNITY AND
POSSIBLY THE REGION

HOSTING CONCERTS SINCE 2011



















RESYSTA - PALE GOLDEN (WWW.RESYSTAUSA.COM)



2 RAINSCREEN (FIBER CEMENT PANELS)

EQUITONE LINEA LT20 (WWW.EQUITONE.COM)



3 CONCRETE BASE

SANDBLASTED CONCRETE WITH VERTICAL SCORING









RESYSTA - PALE GOLDEN (WWW.RESYSTAUSA.COM)



4 MASONRY WALL

ECHELON SPLIT FACE CMU - CHARCOAL SHEFFIELD (HTTPS://WWW.ECHELONMASONRY.COM)




5 CONCRETE BASE

SANDBLASTED CONCRETE WITH VERTICAL SCORING







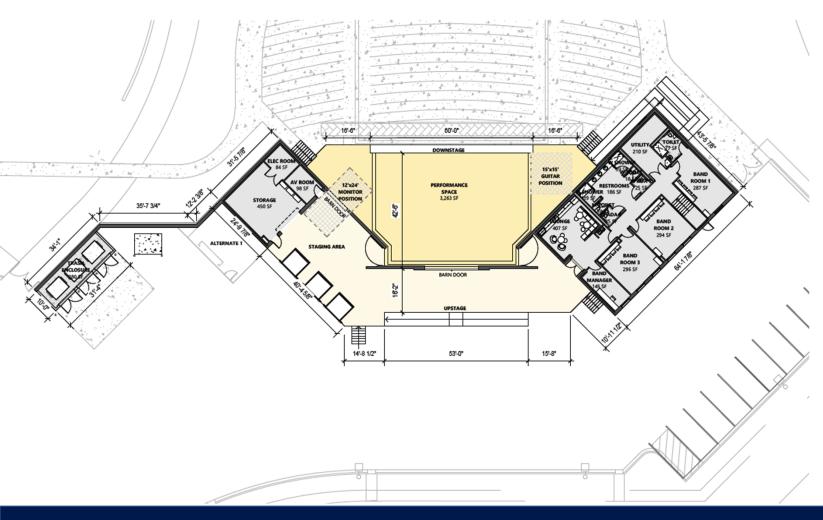

- STAGE: 42' X 60'
- GUITAR & MONITOR POSITIONS
 - STAGING AREA
 - BAND ROOMS: 3
- MANAGERS OFFICE: 1
- HOSPITALITY SUITE (1)
 - RESTROOMS: 4
 - SHOWERS: 2
- STORAGE/ELECTRIAL ROOM

CENTENNIAL PARK WEST STAGE/GREEN ROOMS








PURPOSE: To examine background traffic conditions, assess the impact that the proposed event venue.

Determine if any roadway or access improvements are necessary to accommodate the traffic generated by the proposed event venue.

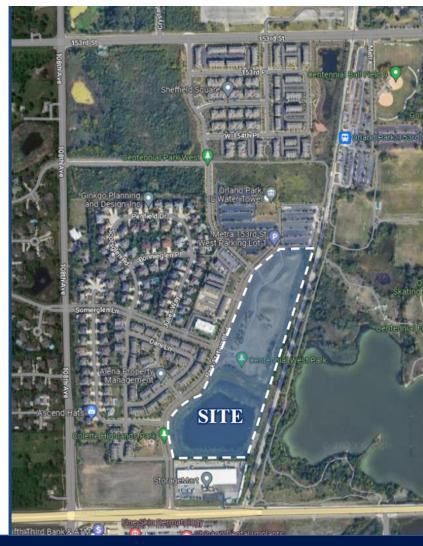





STUDY ANALYSIS:

- Year 2023 Existing Conditions Analyzes the capacity of the existing roadway system using peak hour traffic volumes conducted in 2023.
- Year 2029 Total Conditions Analyzes the capacity of the future roadway system
 using the projected traffic volumes that include the existing traffic volumes,
 ambient traffic growth, and the traffic estimated to be generated by the proposed
 event venue.





AVAILABLE PARKING

METRA WEST: 730

METRA EAST: 670


CENTENNIAL PARK: 1,044







STREET
CLOSURES &
MANAGEMENT

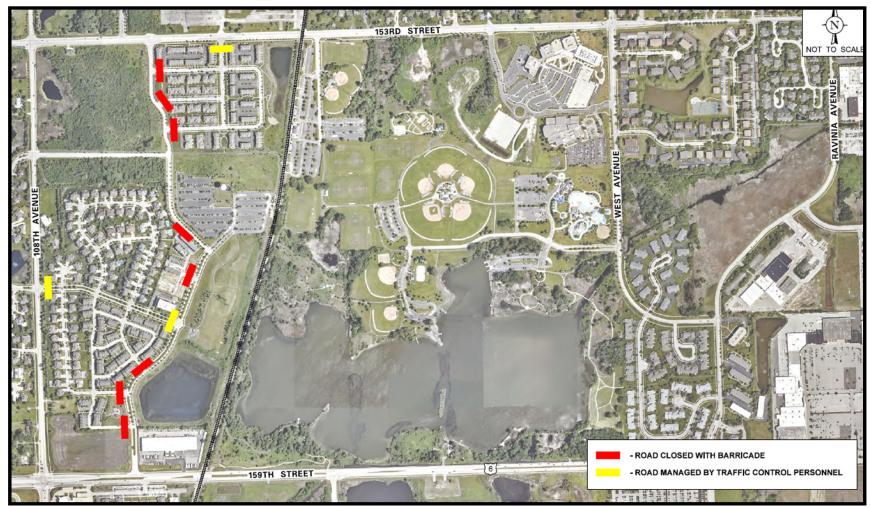





CONCLUSIONS:

- With the implementation of the event traffic management strategies, the roadway system has sufficient reserve capacity to accommodate the traffic generated by the event venue.
- Several of the intersection approaches and movements are projected to operate
 at lower levels of service, which is due to the surging of inbound or outbound event generated
 traffic, particularly after an event.
- Traffic control personnel are proposed to be stationed at many of these intersections to better manage the flow and surging of traffic through the intersections.





CENTENNIAL PARK
WEST CONCERT
SERIES

4TH OF JULY CONCERT & FIREWORKS

TASTE OF ORLAND PARK

WEEKLY MARKET AT THE PARK

MOVIES IN PARK

GREAT PUMPKIN PARTY

ORLAND PARK



REMAINS AVAILABLE
FOR PASSIVE
RECREATION USE
WHEN NOT
SCHEDULDED FOR
EVENTS

INITIALLY, FENCING WILL BE BEHIND STAGE ONLY

CENTENNIAL PARK WEST STAGE





AVAILABLE FOR SPECIAL EVENT PERMITTED USE

NO EARLIER THAN 7AM OR AFTER 12AM BY CODE

TYPICAL USE, CONCLUDES BY 10P OR 11P PLUS CLEAN-UP

CENTENNIAL PARK WEST STAGE











VILLAGE OF ORLAND PARK | CENTENNIAL WEST CONCERT VENUE

