

G & H DEVELOPERS CORPORATION

SUITE 4200 – 200 W. MADISON STREET – CHICAGO, IL 60606-3402 – (312) 332-4172 • FAX (312) 332-4383

**TO: Village of Orland Park
14700 S. Ravinia Avenue
Orland Park, Illinois 60462**

July 1, 2013

INVOICE

**For Services rendered in the relocation of
water main at NWC of 159th & 94th Street**

TOTAL

\$9,798.75

MAYOR
Daniel J. McLaughlin
VILLAGE CLERK
David P. Maher
14700 S. Ravinia Ave.
Orland Park, IL 60462
(708) 403-6100
www.orland-park.il.us



VILLAGE HALL

TRUSTEES
Kathleen M. Fenton
Brad S. O'Halloran
James V. Dodge
Edward G. Schussler III
Patricia A. Gira
Carole Griffin Ruzich

Kevin
P/S
FLO

June 21, 2013

Mr. George Hanus, President
G&H Developers Corporation
200 W. Madison Street
Suite 4200
Chicago, IL 60606-3402

RE: Water Main Relocation
NWC 159th and 94th Avenue
Orland Park, Illinois

Dear Mr. Hanus:

Reference is made to our phone call of earlier today and our recent correspondence of June 17, 2013. As stated before, the purpose of this letter is to attempt to resolve a disputed claim. The Village admits no liability whatsoever in connection with the location of the subject water main and, in fact, any such liability is strenuously denied.

As to your contention that flowable fill is required for the abandoned line, we show that your engineer agreed with us that flowable fill is not necessary in this application, and no reference to a Village Code is mentioned. In discussing with staff, no one can find a Village Code requiring abandoning water main with flowable fill.

In an effort to finalize this matter, the Village will be willing to contribute fifty percent (50%) to the cost of engineering, assuming that the cost for engineering manager replaces the 19.25 hours slated for a principal. That translates to \$3,997.50, fifty percent of which is \$1,998.75. That amount would be added to our previous offer of \$7,800, for a total of \$9,798.75.



We believe that this is a fair offer to resolve this matter expeditiously.

Thanks for your attention to this matter.

Sincerely yours,

Paul G. Grimes
Village Manager

C: Kurt Corrigan
Karie Friling

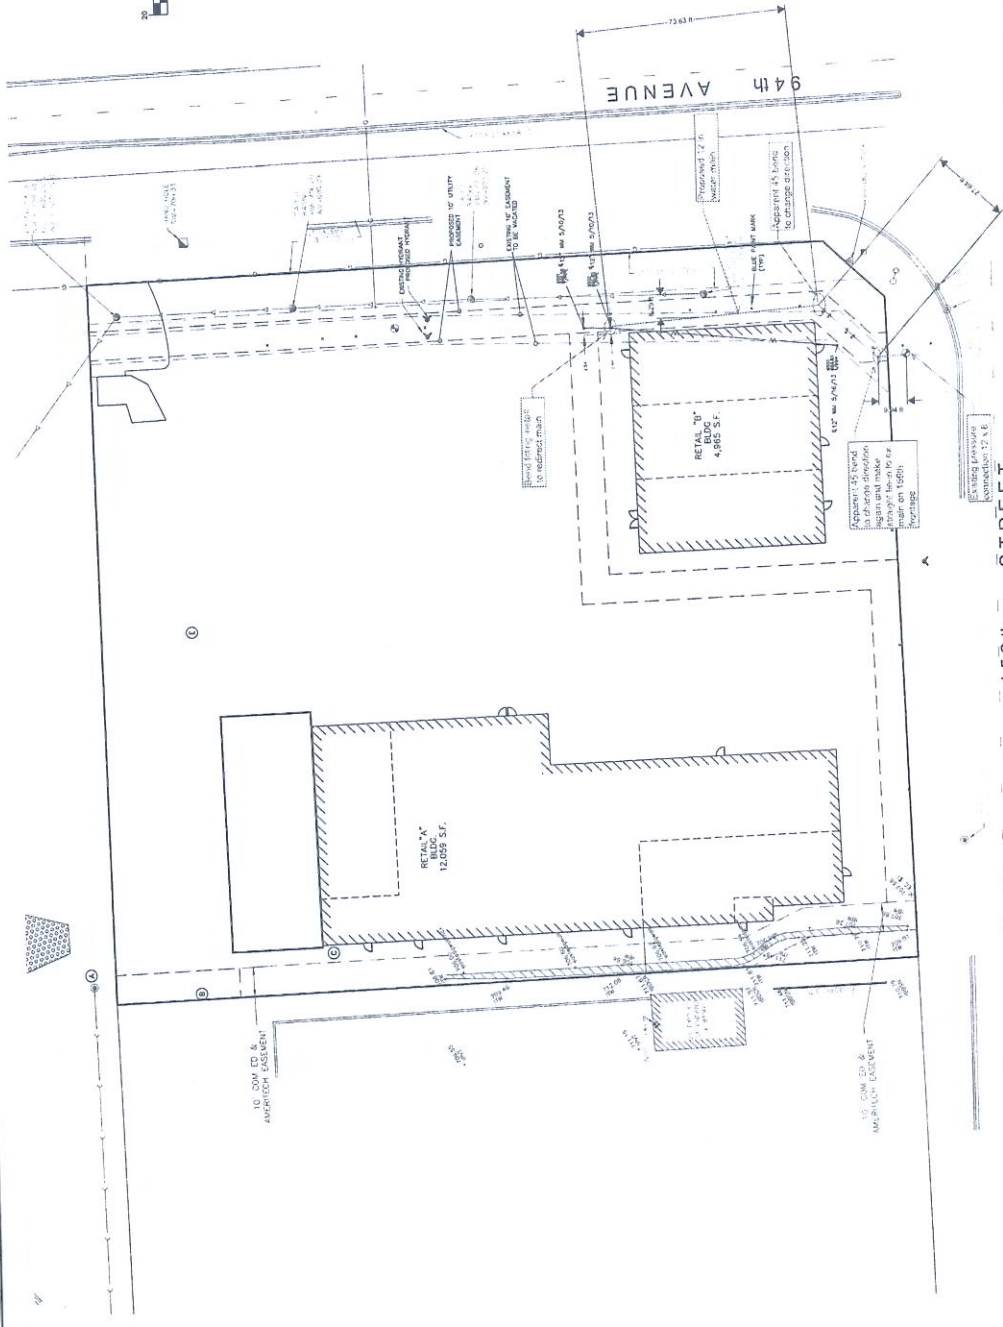

Notes:
 Length of main rebar section approx. 120' +/- plus 1' length.
 Main rebar section is shown to the left of the main rebar section.
 Approx. 6' 1/2" from top of rebar section. At closed joint, which covers a small area.

159th STREET
 (U.S. ROUTE 6)

PROJECT #		PROJECT NAME	
05180		EXISTING WATERMAIN EXHIBIT	
SHEET		ORLAND PARK PLAZA NW 159th ST AND 64th AVE ORLAND PARK, ILLINOIS	
1		1	
DATE		DRAWN BY	
7/17/13		DMS	
SCALE		PROJECT	
1" = 20'		NOV	
REVISIONS		NOV	
NO	DATE	DESCRIPTION	BY

M BRIDE ENGINEERING, INC.
 1100 S. WILSON AVENUE
 SUITE 100
 ORLAND PARK, ILLINOIS 60452
 TEL: 708.584.1100
 FAX: 708.584.1101
 WWW.MBRIDEENGINEERING.COM

THIS DOCUMENT AND THE DATA AND RECORDS
 HEREON ARE THE PROPERTY OF MBRIDE ENGINEERING, INC.
 AND ARE TO BE USED ONLY FOR THE PROJECT AND
 LOCATION SPECIFICALLY IDENTIFIED HEREON.
 NO PART OF THIS DOCUMENT OR RECORDS
 HEREON SHALL BE REPRODUCED OR TRANSMITTED
 IN ANY FORM OR BY ANY MEANS, ELECTRONIC
 OR MECHANICAL, INCLUDING PHOTOCOPYING,
 RECORDING, OR BY ANY INFORMATION STORAGE
 AND RETRIEVAL SYSTEM, WITHOUT THE WRITTEN
 PERMISSION OF MBRIDE ENGINEERING, INC.

RE: 159TH & 94TH - NWC
ORLAND PARK, ILLINOIS

RECAPITULATION OF COSTS

INCURRED AS A RESULT OF ORLAND PARK WATER MAIN BEING LOCATED
OUTSIDE RECORDED EASEMENT

1. RUANE CONSTRUCTION (See attached Exhibit C)	\$17,000
2. MC BRIDE ENGINEERING (See attached Exhibit D)	\$ 4,556
3. 10% OVERHEAD	\$ 2,155
4. 10% PROFIT	<u>\$ 2,155</u>
TOTAL	\$25,866

13,000 w/
DEDUCT OF \$4K
COST OF PIPE GRANT
FILL.

EXHIBIT B



Concrete · Excavating
Conveying · Mass Grading

RUANE CONSTRUCTION INC

8918 Schoger Dr
Naperville, IL 60564

Commercial & Residential

Phone (815) 484-0881
Fax (815) 484-0685

CHANGE ORDER

May 28, 2013

G&H Developers Corporation
200 W Madison, Suite 4200
Chicago, IL 60606
312-332-4172

Village of Orland Park
RE: 159th & 94th Ave

Water Main Relocation

Drycut into existing water main with village shut down on water main
Supply & Install Approx 120LF of 12" CL52 Water Main with all fittings to relocate main
Fill existing line under building with low strength flowable fill

\$17,000⁰⁰

TOTAL ██████████

- *Price does not include retapping 2" line for building #B
- *Price includes starting relocation south of existing tap

~~ALT #1: If line stops are needed for maint shut down~~ ~~ADD \$ 0,700.00~~

- *Price includes testing & chlorination

- NO EXTRAS -

All work to be performed in a good and workmanlike manner. Our work is covered by worker's compensation and public liability insurance. Any alteration or deviation from the plans and specifications will be added to or deducted from the sum quoted in this contract. All additional agreements must be in writing. Prices as quoted are valid for thirty (30) days. Payment terms are thirty (30) days from the invoice date. Purchaser agrees to pay all fees and costs of collection. 1½% per month interest on past due accounts (18% APR).

Date: 6-11-13

Respectfully Submitted: Mark Ruane
Ruane Construction

Accepted By: _____
Signature Print

PLEASE FAX SIGNED OF THIS PROPOSAL TO: RUANE CONST. @ (815) 464-0685

CONTRACTOR ASSUMES RESPONSIBILITY OF FULFILLING THE "SUBCONTRACTORS AWARD AND REQUIREMENTS LETTER"
 CONTRACTORS WILL BE EXPECTED TO CLEAN UP THEIR DEBRIS. NO EXTRAS
 UNDER THIS CONTRACT EACH CONTRACTOR ASSUMES RESPONSIBILITY AND SUPERVISION OF THEIR OWN HEALTH AND SAFETY ON THE JOB.
 CONTRACTOR AGREES TO BE REGISTERED WITHIN 48 HOURS WITH THE LOCAL MUNICIPALITY AFTER BEING AWARDED THE CONTRACT.

EXHIBIT "C"

McBRIDE ENGINEERING, INC.
CIVIL ENGINEERS & SURVEYORS



June 11, 2013

21032

Aetna Development Corp.
200 W. Madison St., Suite 4200
Chicago, IL 60606

INVOICE NO. _____

A FINANCE CHARGE OF 1 1/4% PER MONTH
WILL BE ASSESSED AGAINST ALL OUT-
STANDING BALANCES AFTER 30 DAYS FROM
THE DATE OF THE INVOICE

I N V O I C E
FOR SERVICES RENDERED

Date	Description	Amount
	Orland Park Plaza - 159 th & 94 th Avenue Orland Park, Illinois MEI #06180	
	W.O. #5167	
	<u>ADDITIONAL SERVICES - REGARDING WATERMAIN LOCATION</u>	
5/09/13 thru 6/11/13	RESEARCH EXISTING WATERMAIN LOCATION, ADDRESS WATERMAIN LOCATION ISSUE, EASEMENT DOCUMENT STATUS; CONFERENCE CALL WITH VILLAGE ENGINEER AND CLIENT; CREATE EXHIBIT DOCUMENT FOR WATERMAIN VERSUS BUILDING FOUNDATION AND EXISTING EASEMENT LOCATIONS; LOCATE WATERMAIN; DISCUSS EASEMENT LOCATION WITH CLIENT, FOLLOWUP WITH VILLAGE ENGINEER REGARDING PLAT OF VACATION; REVIEW WATERMAIN RELOCATION ROUTE PROPOSED BY VILLAGE, DISCUSS STRUCTURAL AND EASEMENT CONCERNS WITH ARCHITECT; FOLLOWUP WITH VILLAGE, CHECK CONTRACTOR COSTS; ADDRESS SOIL TESTING QUESTION; ADDITIONAL PHONE DISCUSSIONS WITH VILLAGE ENGINEER, CLIENT AND ARCHITECT REGARDING COSTS; PLAT REVISIONS AND TIMING; EMAILS AND CALLS REGARDING J.U.L.I.E. RULES AND REGULATIONS FOR ACCURATE LOCATIONS; CHECK STATUS WITH VILLAGE ENGINEER; DISCUSS PUBLIC WORKS' POINT OF VIEW WITH VILLAGE ENGINEER	
	Principal	
	19.25 Hrs @ \$175/hr	\$3,368.75
	Engineering Manager	
	4 Hrs @ \$146/hr	584.00
	Sr. Professional Land Surveyor	
	4 Hrs @ \$123/hr	492.00
	Survey Crew	
	.75 Hr @ \$148/hr	<u>111.00</u>
	TOTAL AMOUNT DUE THIS INVOICE	<u>\$4,555.75</u>

Handwritten notes:
K123
2/11/13
7800
- 11,777
= 19,177.50

EXHIBIT D
