

Bid Proposal
for
Village of Orland Park
Water Meter Replacement Program Installation
RFP #22-062

281 River Oaks Drive, Calumet City, IL 60409
(708) 868-0074/(708) 868-0102 Fax
IDPH 055-008908



Calumet City Plumbing & Heating Co., Inc.
 Bid Proposal for Water Meter Replacement Program Installation
 RFP #22-062

TABLE OF CONTENTS

SECTION 1 – REQUIRED SUBMISSIONS	
Proposer Summary Sheet	4
Certificate of Compliance	6-10
References	12
Insurance Requirements	14-16
Unit Price Sheet	18
Bid Bond	20-21
SECTION 2 – TECHNICAL PROPOSAL	
Meter Installation Experience	24-27
Operating History	29-31
Qualifications	33-42
Understanding of the Village’s Meter Conversion Process	44-60
Proposed Fee	62
SECTION 3 – PROPOSED SCHEDULE OF INSTALLATION WORK	
Proposed Schedule of Installation	64

**Bid Tabulation page numbers on the top right of document*

SECTION 1 – REQUIRED SUBMISSIONS

PROPOSER SUMMARY SHEET

PROPOSER SUMMARY SHEET
RFP 22-062
Water Meter Replacement Program Installation

Business Name: Calumet City Plumbing & Heating Co., Inc.

Street Address: 281 River Oaks Drive

City, State, Zip: Calumet City, IL 60409

Contact Name: Moe Giglio

Title: President

Phone: (708) 868-0074 Fax: (708) 868-0102

E-Mail address: moe@ccp1967.com

Price Proposal

Total Bid Price \$3,274,990.00

AUTHORIZATION & SIGNATURE

Proposing Firm:

Name of Authorized Signee: Moe Giglio

Signature of Authorized Signee: 

Title: President Date: 10/20/2022

CERTIFICATE OF COMPLIANCE


ORLAND PARK
CERTIFICATE OF COMPLIANCE

Proposals shall complete this Certificate of Compliance. Failure to comply with all submission requirements may result in a determination that the Proposals is not responsible.

The undersigned Moe Giglio ,
(Enter Name of Person Making Certification)

as President
(Enter Title of Person Making Certification)

and on behalf of Calumet City Plumbing & Heating Co., Inc. ,
(Enter Name of Business Organization)

certifies that Proposers is:

1) **A BUSINESS ORGANIZATION:** Yes [X] No []

Federal Employer I.D. #: 36-2613764
(or Social Security # if a sole proprietor or individual)

The form of business organization of the Proposer is (*check one*):

Sole Proprietor
 Independent Contractor (*Individual*)
 Partnership
 LLC
 Corporation Illinois 4/11/1967
(State of Incorporation) (Date of Incorporation)

2) **STATUS OF OWNERSHIP**

Illinois Public Act 102-0265, approved August 2021, requires the Village of Orland Park to collect "Status of Ownership" information. This information is collected for reporting purposes only. Please check the following that applies to the ownership of your business and include any certifications for the categories checked with the proposal. Business ownership categories are as defined in the Business Enterprise for Minorities, Women, and Persons with Disabilities Act, 30 ILCS 575/0.01 *et seq.*

Minority-Owned [] Small Business [X] (SBA standards)
 Women-Owned [] Prefer not to disclose []
 Veteran-Owned [] Not Applicable []
 Disabled-Owned []

How are you certifying? Certificates Attached [] Self-Certifying [X]

STATUS OF OWNERSHIP FOR SUBCONTRACTORS

This information is collected for reporting purposes only. Please check the following that applies to the ownership of subcontractors.

Minority-Owned [] Small Business [] (SBA standards)
 Women-Owned [] Prefer not to disclose []
 Veteran-Owned [] Not Applicable [X]
 Disabled-Owned []

3) **AUTHORIZED TO DO BUSINESS IN ILLINOIS:** Yes [X] No []

The Proposer is authorized to do business in the State of Illinois.

4) **ELIGIBLE TO ENTER INTO PUBLIC CONTRACTS:** Yes [X] No []

The Proposer is eligible to enter into public contracts, and is not barred from contracting with any unit of state or local government as a result of a violation of either Section 33E-3, or 33E-4 of the Illinois Criminal Code, or of any similar offense of "bid-rigging" or "bid-rotating" of any state or of the United States.

5) **SEXUAL HARASSMENT POLICY COMPLIANT:** Yes [X] No []

Please be advised that Public Act 87-1257, effective July 1, 1993, 775 ILCS 5/2-105 (A) has been amended to provide that every party to a public contract must have a written sexual harassment policy in place in full compliance with 775 ILCS 5/2-105 (A) (4) and includes, at a minimum, the following information:

(I) the illegality of sexual harassment; (II) the definition of sexual harassment under State law; (III) a description of sexual harassment, utilizing examples; (IV) the vendor's internal complaint process including penalties; (V) the legal recourse, investigative and complaint process available through the Department of Human Rights (the "Department") and the Human Rights Commission (the "Commission"); (VI) directions on how to contact the Department and Commission; and (VII) protection against retaliation as provided by Section 6-101 of the Act. (Illinois Human Rights Act). (emphasis added). Pursuant to 775 ILCS 5/1-103 (M) (2002), a "public contract" includes "...every contract to which the State, any of its political subdivisions or any municipal corporation is a party."

6) **EQUAL EMPLOYMENT OPPORTUNITY COMPLIANT:** Yes [X] No []

During the performance of this Project, Proposer agrees to comply with the "Illinois Human Rights Act", 775 ILCS Title 5 and the Rules and Regulations of the Illinois Department of Human Rights published at 44 Illinois Administrative Code Section 750, et seq.

The Proposer shall:

(I) not discriminate against any employee or applicant for employment because of race, color, religion, sex, marital status, national origin or ancestry, age, or physical or mental handicap unrelated to ability, or an unfavorable discharge from military service; (II) examine all job classifications to determine if minority persons or women are underutilized and will take appropriate affirmative action to rectify any such underutilization; (III) ensure all solicitations or

advertisements for employees placed by it or on its behalf, it will state that all applicants will be afforded equal opportunity without discrimination because of race, color, religion, sex, marital status, national origin or ancestry, age, or physical or mental handicap unrelated to ability, or an unfavorable discharge from military service; (IV) send to each labor organization or representative of workers with which it has or is bound by a collective bargaining or other agreement or understanding, a notice advising such labor organization or representative of the Vendor’s obligations under the Illinois Human Rights Act and Department’s Rules and Regulations for Public Contract; (V) submit reports as required by the Department’s Rules and Regulations for Public Contracts, furnish all relevant information as may from time to time be requested by the Department or the contracting agency, and in all respects comply with the Illinois Human Rights Act and Department’s Rules and Regulations for Public Contracts; (VI) permit access to all relevant books, records, accounts and work sites by personnel of the contracting agency and Department for purposes of investigation to ascertain compliance with the Illinois Human Rights Act and Department’s Rules and Regulations for Public Contracts; and (VII) include verbatim or by reference the provisions of this Equal Employment Opportunity Clause in every subcontract it awards under which any portion of this Agreement obligations are undertaken or assumed, so that such provisions will be binding upon such subcontractor.

In the same manner as the other provisions of this Agreement, the Proposer will be liable for compliance with applicable provisions of this clause by such subcontractors; and further it will promptly notify the contracting agency and the Department in the event any subcontractor fails or refuses to comply therewith. In addition, the Proposer will not utilize any subcontractor declared by the Illinois Human Rights Department to be ineligible for contracts or subcontracts with the State of Illinois or any of its political subdivisions or municipal corporations.

“Subcontract” means any agreement, arrangement or understanding, written or otherwise, between the Proposer and any person under which any portion of the Proposer’s obligations under one or more public contracts is performed, undertaken or assumed; the term “subcontract”, however, shall not include any agreement, arrangement or understanding in which the parties stand in the relationship of an employer and an employee, or between a Proposer or other organization and its customers.

In the event of the Proposer’s noncompliance with any provision of this Equal Employment Opportunity Clause, the Illinois Human Right Act, or the Rules and Regulations for Public Contracts of the Department of Human Rights the Proposer may be declared non-responsible and therefore ineligible for future contracts or subcontracts with the State of Illinois or any of its political subdivisions or municipal corporations, and this agreement may be canceled or avoided in whole or in part, and such other sanctions or penalties may be imposed or remedies involved as provided by statute or regulation.

7) **PREVAILING WAGE COMPLIANCE:** Yes [X] No []

In the manner and to the extent required by law, this RFP is subject to the Illinois Prevailing Wage Act and to all laws governing the payment of wages to laborers, workers and mechanics of a Proposer or any subcontractor of a Proposer bound to this agreement who is performing services covered by this contract. If awarded the Contract, per 820 ILCS 130 et seq. as amended, Proposer shall pay not less than the prevailing hourly rate of wages, the generally prevailing rate of hourly wages for legal holiday and overtime work, and the prevailing hourly rate for welfare and other benefits as determined by the Illinois Department of Labor or the Village and as set forth in the schedule of prevailing wages for this contract to all laborers,

workers and mechanics performing work under this contract (available at <https://www2.illinois.gov/idol/Laws-Rules/CONMED/Pages/Rates.aspx>).

The undersigned Proposer further stipulates and certifies that it has maintained a satisfactory record of Prevailing Wage Act compliance with no significant Prevailing Wage Act violations for the past three (3) years.

Certified Payroll. The Illinois Prevailing Wage Act requires any contractor and each subcontractor who participates in public works to file with the Illinois Department of Labor (IDOL) certified payroll for those calendar months during which work on a public works project has occurred. The Act requires certified payroll to be filed with IDOL no later than the 15th day of each calendar month for the immediately preceding month through the Illinois Prevailing Wage Portal—an electronic database IDOL has established for collecting and retaining certified payroll. The Portal may be accessed using this link: <https://www2.illinois.gov/idol/Laws-Rules/CONMED/Pages/certifiedtranscriptofpayroll.aspx>. The Village reserves the right to withhold payment due to Contractor until Contractor and its subcontractors display compliance with this provision of the Act.

8) **PARTICIPATION IN APPRENTICESHIP AND TRAINING PROGRAM:** Yes No

Proposer participates in apprenticeship and training programs applicable to the work to be performed on the project, which are approved by and registered with the United States Department of Labor's Office of Apprenticeship.

Name of A&T Program: Plumbers' Joint Apprenticeship Committee Local 130, U.A. (Registration No. IL015030003)

Brief Description of Program: The JAC is a five year program which includes classroom instruction

and on the job field training. During the first three years, Apprentices work on the job four days per

week and attend one day of classroom instruction. During the 4th and 5th years, apprentices have on

the job training 5 days per week and attend night school classes. Apprentices learn to safely, correctly, and efficiently install and maintain plumbing systems, including residential and service plumbing, fixture installation, waste and vent piping, underground water supply, storm water and sewer drainage.

9) **TAX COMPLIANT:** Yes No

Proposer is current in the payment of any tax administered by the Illinois Department of Revenue, or if it is not: (a) it is contesting its liability for the tax or the amount of tax in accordance with procedures established by the appropriate Revenue Act; or (b) it has entered into an agreement with the Department of Revenue for payment of all taxes due and is currently in compliance with that agreement.

AUTHORIZATION & SIGNATURE:

I certify that I am authorized to execute this Certificate of Compliance on behalf of the Proposer set forth on the Proposer Summary Sheet, that I have personal knowledge of all the information set forth herein and that all statements, representations, that the proposal is genuine and not collusive, and information provided in or with this Certificate are true and accurate.

The undersigned, having become familiar with the Project specified in this RFP, proposes to provide and furnish all of the labor, materials, necessary tools, expendable equipment and all utility and transportation services necessary to perform and complete in a workmanlike manner all of the work required for the Project.

ACKNOWLEDGED AND AGREED TO:



Signature of Authorized Officer

Moe Giglio

Name of Authorized Officer

President

Title

10/20/2022

Date

REFERENCES

REFERENCES

Provide three (3) references for which your organization has performed similar work.

Proposer's Name: Calumet City Plumbing & Heating Co., Inc.
(Enter Name of Business Organization)

1. ORGANIZATION Justice-Willow Springs Water Commission
ADDRESS 7000 S. Archer Rd., Justice, IL 60458
PHONE NUMBER (708) 458-7010
CONTACT PERSON Colleen Kelly, Executive Director
YEAR OF PROJECT 2021-2022

2. ORGANIZATION City of Joliet
ADDRESS 150 W. Jefferson Street, Joliet, IL 60432
PHONE NUMBER (815) 724-4220
CONTACT PERSON Jonathan Hall
YEAR OF PROJECT 2020-2022

3. ORGANIZATION City of Naperville
ADDRESS 1200 W. Ogden Avenue, Naperville, IL 60563
PHONE NUMBER (630) 420-6134
CONTACT PERSON Angie Keller
YEAR OF PROJECT 2019-2020

INSURANCE REQUIREMENTS


ORLAND PARK
INSURANCE REQUIREMENTS

Please provide a policy Specimen Certificate of Insurance showing current coverage's along with this form

WORKERS' COMPENSATION & EMPLOYER LIABILITY

Full Statutory Limits - Employers Liability
 \$500,000 – Each Accident \$500,000 – Each Employee
 \$500,000 – Policy Limit
 Waiver of Subrogation in favor of the Village of Orland Park

AUTOMOBILE LIABILITY (ISO Form CA 0001)

\$1,000,000 – Combined Single Limit Per Occurrence
 Bodily Injury & Property Damage

GENERAL LIABILITY (Occurrence basis) (ISO Form CG 0001)

\$1,000,000 – Combined Single Limit Per Occurrence
 Bodily Injury & Property Damage
 \$2,000,000 – General Aggregate Limit
 \$1,000,000 – Personal & Advertising Injury
 \$2,000,000 – Products/Completed Operations Aggregate
Additional Insured Endorsements: *(not applicable for Goods Only)*
 ISO CG 20 10 or CG 20 26
and
 CG 20 01 Primary & Non-Contributory
 Blanket Waiver of Subrogation in favor of the Village of Orland Park

CG 20 37 Additional Insured – Completed Operations (provide if box is checked)

In addition to the above, please provide the following coverage, if box is checked.

- LIABILITY UMBRELLA (Follow Form Policy)**
- \$1,000,000 – Each Occurrence \$1,000,000 – Aggregate
- \$2,000,000 – Each Occurrence \$2,000,000 – Aggregate
- Other: _____

EXCESS MUST COVER: General Liability, Automobile Liability, Employers' Liability

PROFESSIONAL LIABILITY

- \$1,000,000 Limit – Claims Made Form, Indicate Retroactive Date
- \$2,000,000 Limit – Claims Made Form, Indicate Retroactive Date
- Other: _____
 Deductible not-to-exceed \$50,000 without prior written approval

BUILDERS RISK

Completed Property Full Replacement Cost Limits – Structures under construction

ENVIRONMENTAL IMPAIRMENT/POLLUTION LIABILITY

\$1,000,000 Limit for bodily injury, property damage and remediation costs resulting from a pollution incident at, on or mitigating beyond the job site

CYBER LIABILITY


\$1,000,000 Limit per Data Breach for liability, notification, response, credit monitoring service costs, and software/property damage

Any insurance policies providing the coverages required of the Consultant, excluding Professional Liability, shall be specifically endorsed to identify "The Village of Orland Park, and their respective officers, trustees, directors, officials, employees, volunteers and agents as Additional Insureds on a primary/non-contributory basis with respect to all claims arising out of operations by or on behalf of the named insured." The required

Additional Insured coverage shall be provided on the Insurance Service Office (ISO) CG 20 10 or CG 20 26 endorsements or an endorsement at least as broad as the above noted endorsements as determined by the Village of Orland Park. Any Village of Orland Park insurance coverage shall be deemed to be on an excess or contingent basis as confirmed by the required (ISO) CG 20 01 Additional Insured Primary & Non-Contributory Endorsement. The policies shall also contain a Waiver of Subrogation in favor of the Additional Insureds in regard to General Liability and Workers' Compensation coverage. The certificate of insurance shall also state this information on its face. Any insurance company providing coverage must hold an A-, VII rating according to Best's Key Rating Guide. Each insurance policy required shall have the Village of Orland Park expressly endorsed onto the policy as a Cancellation Notice Recipient. Should any of the policies be cancelled before the expiration date thereof, notice will be delivered in accordance with the policy provisions. Permitting the contractor, or any subcontractor, to proceed with any work prior to our receipt of the foregoing certificate and endorsements shall not be a waiver of the contractor's obligation to provide all the above insurance.

Consultant agrees that prior to any commencement of work to furnish evidence of Insurance coverage providing for at minimum the coverages, endorsements and limits described above directly to the Village of Orland Park, 14700 S. Ravinia Avenue, Orland Park, IL 60462. Failure to provide this evidence in the time frame specified and prior to beginning of work may result in the termination of the Village's relationship with the contractor.

ACCEPTED & AGREED THIS 20th DAY OF October, 2022



Signature
Moe Giglio, President

Printed Name & Title

Authorized to execute agreements for:
Calumet City Plumbing & Heating Co., Inc.

Name of Company

UNIT PRICE SHEET



ORLAND PARK

BIDDER UNIT PRICE SHEET

RFP 22-062 Water Meter Replacement Program Installation

The undersigned, having become familiar with the Documents, Construction Plans, and Specifications on file in the office of the Owner as designated in the Request for Proposals, hereby proposes to provide and furnish all of the labor, materials, necessary tools, expendable equipment and all utility and transportation services necessary to perform and complete in a workmanlike manner all of the work required for and the work described in the following schedule in connection with the Meter Replacement Program Installation contract.

No	Item	Quantity*	Unit	Unit Price	Amount
Water Meter Installation					
1	Installation of 3/4" Sensus iPERL Water Meter	13481	EACH	\$122.00	\$1,644,682.00
2	Installation of 3/4" Sensus ALLY Water Meter	2291	EACH	\$122.00	\$279,502.00
3	Installation of 1" Sensus iPERL Water Meter	2805	EACH	\$122.00	\$342,210.00
4	Installation of 1-1/2" Sensus OMNI+ Water Meter	317	EACH	\$450.00	\$142,650.00
5	Installation of 2" Sensus OMNI+ Water Meter	286	EACH	\$485.00	\$138,710.00
6	Installation of 3" Sensus OMNI+ Water Meter	60	EACH	\$795.00	\$47,700.00
7	Installation of 4" Sensus OMNI+ Water Meter	90	EACH	\$900.00	\$81,000.00
8	Project and Data Management	1	LSUM	\$598,536.00	\$598,536.00 *
Water Meter Installation Subtotal					\$3,274,990.00

*Quantity is an estimation; final project pricing shall be determined by actual meter numbers at the price per item as listed.

No	Item	Quantity	Unit	Unit Price	
Contingency Items **					
9	3/4" Ball Valve & Installation	1	EACH	\$225.00	
10	1" Ball Valve & Installation	1	EACH	\$245.00	
11	3/4" Brass Water Meter Coupling & Installation	1	EACH	\$85.00	
12	1" Brass Water meter Coupling & Installation	1	EACH	\$90.00	
13	1-1/2" Brass Water Meter Coupling & Installation	1	EACH	\$285.00	
14	2" Brass Water Meter Coupling & Installation	1	EACH	\$365.00	
15	Grounding Strap Kit (Brass clamps with #4G copper wire)	1	EACH	\$26.00	
16	Vault/Pit Set Meter Repair **	1	EACH	\$365.00	
17	Concrete Restoration	1	EACH	\$1,495.00	
18	Scheduling appointments outside of the standardized installation time	1	EACH	\$165.00	
19	Replace wiring between Touchpads/Transmitters and Meters	1	EACH	\$125.00	

**Contingency items include Materials and Installation. Installation is to be priced for Standard Pit Sets and like-for-like exchange. Quantity shall be submitted monthly with documentation for payment.

* Project and Data Management: Pricing based on 50% to be released on the first pay application, 25% at substantial completion, and 25% at final pay application.

Total = \$ 3,274,990.00

(Enter this amount as Total Proposal Price on Proposal Summary Sheet)

** Vault/Pit Set Repair: Pricing is based on Meter sizes from 5/8" to 1". Anything larger will be priced based on meter size and location.

The foregoing total shall be the basis for establishing the amount of the labor and payment and performance bonds and is not to be construed as a lump sum Contract Price. The actual number of units used will determine the final cost of the project.

Proposer/Contractor:

Firm Name: Calumet City Plumbing & Heating Co., Inc.

Signed:

Title: Moe Giglio, President

Dated: 10/20/2022

BID BOND

Document A310™ – 2010

Conforms with The American Institute of Architects AIA Document 310

Bid Bond

CONTRACTOR:

(Name, legal status and address)

Calumet City Plumbing & Heating Co., Inc.
281 River Oaks Drive
Calumet City, IL 60409

OWNER:

(Name, legal status and address)

Village of Orland Park
14700 Ravina Avenue
Orland Park, IL 60462

SURETY:

(Name, legal status and principal place of business)

Travelers Casualty and Surety Company of America

One Tower Square
Hartford, CT 06183
Mailing Address for Notices
Same as above

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

Any singular reference to Contractor, Surety, Owner or other party shall be considered plural where applicable.

BOND AMOUNT: 10% Ten Percent of Amount Bid

PROJECT:

(Name, location or address, and Project number, if any)

Water Meter Replacement Program Installation

The Contractor and Surety are bound to the Owner in the amount set forth above, for the payment of which the Contractor and Surety bind themselves, their heirs, executors, administrators, successors and assigns, jointly and severally, as provided herein. The conditions of this Bond are such that if the Owner accepts the bid of the Contractor within the time specified in the bid documents, or within such time period as may be agreed to by the Owner and Contractor, and the Contractor either (1) enters into a contract with the Owner in accordance with the terms of such bid, and gives such bond or bonds as may be specified in the bidding or Contract Documents, with a surety admitted in the jurisdiction of the Project and otherwise acceptable to the Owner, for the faithful performance of such Contract and for the prompt payment of labor and material furnished in the prosecution thereof; or (2) pays to the Owner the difference, not to exceed the amount of this Bond, between the amount specified in said bid and such larger amount for which the Owner may in good faith contract with another party to perform the work covered by said bid, then this obligation shall be null and void, otherwise to remain in full force and effect. The Surety hereby waives any notice of an agreement between the Owner and Contractor to extend the time in which the Owner may accept the bid. Waiver of notice by the Surety shall not apply to any extension exceeding sixty (60) days in the aggregate beyond the time for acceptance of bids specified in the bid documents, and the Owner and Contractor shall obtain the Surety's consent for an extension beyond sixty (60) days.

If this Bond is issued in connection with a subcontractor's bid to a Contractor, the term Contractor in this Bond shall be deemed to be Subcontractor and the term Owner shall be deemed to be Contractor.

When this Bond has been furnished to comply with a statutory or other legal requirement in the location of the Project, any provision in this Bond conflicting with said statutory or legal requirement shall be deemed deleted herefrom and provisions conforming to such statutory or other legal requirement shall be deemed incorporated herein. When so furnished, the intent is that this Bond shall be construed as a statutory bond and not as a common law bond.

Signed and sealed this 20th day of October, 2022.

Calumet City Plumbing & Heating Co., Inc.

(Principal)

(Seal)

By:

(Title) Moe Giglio, President

Travelers Casualty and Surety Company of America

(Surety)


(Seal)

By:

(Title) Kristen Schmidt, Attorney-in-Fact

(Witness)

(Witness) Dave Roth



SECTION 2 – TECHNICAL PROPOSAL

METER INSTALLATION EXPERIENCE

281 River Oaks Drive
P.O. Box #150
Calumet City, IL 60409



Tel: 708-868-0074
Fax: 708-868-0102
Web: ccp1967.com

October 2022

Back in 1997, we received a call around 9 PM about a water leak inside the Kroch's & Brentano's Book Store here in Calumet City, IL. The City of Calumet City had replaced their 3" water meter by others earlier that day. The Installer had used a "Quick Flange," it blew apart, flooded the Book Store & since that night we have been in the water meter replacement business.

Calumet City Plumbing (CCP) has grown the Water Meter Replacement business for more than 20 years. We have installed Badger, Kamstrup, Master, Neptune, Sensus & Meters with Aclara, Orion, & Sensus Smart Points. Our experience is vast. We have Project Managers who are not only Licensed Plumbers but experienced in more than meter replacements-Specifically the repairs that often go along with the work. We also have internal Administrative Staffing assigned to our Meter work. Our installers are committed, thoroughly trained, & enjoy the work they do. They realize the importance of being on time, working professionally & the responsibility they have as a reflection of our Shop & your Agency.

Our Partnership with ME Simpson (MES) has also flourished. As the technology has changed/improved, MES has continued to raise the bar. Offering On-Line Scheduling & data documentation-Photos, etc. well before others. Their friendly Customer Service Representatives are committed to making your replacement project successful.

In 2003 when we bid the Arlington Heights Water Meter Replacement Project there was some concern as to whether we could "handle" the Job. 18,000 Meters over 3 years. We were complete in 2 years. We continued to "run strong" straight through 2009 when the 2008 Recession caught up. We weathered & in 2012 started ramping back up. Since 2012 we have completed numerous, smaller projects, often simultaneously. I can say from experience it's a lot tougher to run a bunch of smaller jobs than it is to run 1 larger one. Currently, CCP is fast approaching our 100,000-water meter replacement. See attached for completed project name and numbers of meters installed.

We have a dedicated Fleet of mini vans & panel van trucks for our Water Meter Replacement Work. Our Warehouse is fully capable of storing thousands of meters at any time.

Thank you for the opportunity to provide our Response to your RFP.

Respectfully,


Michael Giglio
Vice President

Biographies/Resumes of Key Individuals

MOE GIGLIO is the third-generation President of the Calumet City Plumbing Co., Inc. Moe has been employed with Calumet City Plumbing since 2015 where he has increasingly taken on more roles and currently is Director of Operations and Safety. Moe oversees all field and shop operations, including equipment and inventory control and reviewing truck plumbing and safety equipment for upgrades/new equipment needs. Moe manages and conducts semi-monthly field safety meeting and conducts various safety training programs, including confined space entry, fork truck training, groundwater, wells and pumping equipment, excavation. Additionally, Moe performs jobsite safety checks and reviews. Moe is a licensed Illinois plumber and numerous certifications, including confined space entry, OSHA 30, EPA lead renovator, OSHA excavation competent person.

MICHAEL GIGLIO is the second-generation Vice President and Owner of Calumet City Plumbing Co., Inc. since 1993. Michael attended Roosevelt University & achieved his BA in Business Management in 1987. As a licensed Plumber, Cross Connection Control Device Inspector, & Plumbing Contractor in both Illinois & Indiana, Michael has been very active in both his company as well as the regional plumbing industry. Michael is well verse in all types of plumbing, including new/renovation interior plumbing, new/repair sewer/water main work, and meter installation. Over the past decade he more than doubled the square footage of the current location and invested in tools and equipment which now has a replacement value in excess of two million dollars. From 1994-1996, Michael served as a Trustee of the Plumbing Council of Chicago, an Industry fund for the promotion of the plumbing industry. He also served as a Board Member of the Plumbing Contractors Assoc. of Chicagoland & Cook County. Other memberships include the American Public Works Assoc., American Water Works Assoc., Underground Contractors Assoc., Calumet Area Industrial Commission, & South Suburban Mayors & Managers Assoc.

JEFF CURTIS is a project manager/estimator and supervises Calumet City Plumbing's Meter Division. Jeff estimates and manages all meter projects, including meter replacements, MXU exchanges and AMR installations. Jeff has been employed with Calumet City Plumbing since 2017. As a licensed Illinois and Chicago Plumber, Cross Connection Control Device Inspector, and certified Illinois Plumbing Inspector, Jeff has become a local reference to both municipal public works directors and civil engineers regarding meter replacements/installations. Prior to coming to Calumet City Plumbing, Jeff owned a plumbing company in northeast Illinois, where he managed, estimated, and performed all types of residential and commercial plumbing services. Jeff is active in the regional plumbing industry. Jeff is a current member and Recording Secretary of the I.P.I.A. Chapter 2 Tri-County Illinois Inspectors Association.



PROJECT CONTACT INFORMATION

LINE NO	CONTACT NAME	TITLE	Meter Installation & Management Experience		OFFICE			EMAIL ADDRESS
			OFFICE PHONE	EXT	CELL PHONE	EXT		
1	MOE GIGLIO	PRESIDENT	10 Years	708-868-0074	621	708-417-2514	MOE@CCP1967.COM	
2	MICHAEL GIGLIO	VICE PRESIDENT	25 Years	708-868-0074	699	708-243-3821	MG@CCP1967.COM	
3	JEFFREY CURTIS	PROJECT MANAGER	20 Years	708-868-0074	611	708-417-4061	JC@CCP1967.COM	
4	DENNIS SPEAR	PROJECT MANAGER/ FIELD	25 Years	708-868-0074	616	219-765-9948	DS@CCP1967.COM	
5	RODNEY TRACY	PROJECT MANAGER	6 Years	708-868-0074	652	815-821-5893	RT@CCP1967.COM	
6	JEANNETTE SALINAS	ASSIST. P/M	1 Year	708-868-0074	615		JS@CCP1967.COM	
7	JESSICA FLORES	SCHEDULING COORDINATOR	4 Years	708-868-0074	614		JF@CCP1967.COM	
8	AGUSTIN AVITIA	INSTALLER	2 Years			219-671-7505	AAVI@CCP1967.COM	
9	JONATHAN BOREM	INSTALLER	2 Years			815-735-0662	JBOR@CCP1967.COM	
10	JESUS CARRENO	INSTALLER	2 Years			815-641-2621	JCAR@CCP1967.COM	
11	JIM COBB	INSTALLER	6 Years			815-690-6552	JCOB@CCP1967.COM	
12	DAN HILLOCK	INSTALLER	2 Years			630-205-6586	DHIL@CCP1967.COM	
13	KARL JONAS	INSTALLER	2 Years			708-601-2463	KJON@CCP1967.COM	
14	RICK LARA	INSTALLER	15 Years			630-205-6586	RLAR@CCP1967.COM	
15	GARRETT MARTINEZ	INSTALLER	2 Years			219-741-7140	GMAR@CCP1967.COM	
16	MICHAEL SZYMANSKI	INSTALLER	4 Years			847-915-1563	MSZY@CCP1967.COM	
17	JULIAN TAFOYA	INSTALLER	1 Year			219-741-7140	JTAF@CCP1967.COM	
18	ZACH TRAYNOR	INSTALLER	6 Years			708-571-6616	ZTRA@CCP1967.COM	

Calumet City Plumbing

281 River Oaks Dr, Calumet City, IL 60409

281 River Oaks Drive
P.O. Box #150
Calumet City, IL 60409



Tel: 708-868-0074
Fax: 708-868-0102
Web: ccp1967.com

EH0193877

Illinois Department of PUBLIC HEALTH

LICENSE, PERMIT, CERTIFICATION, REGISTRATION

The person, firm or corporation whose name appears on this certificate has complied with the provisions of the Illinois statutes and/or rules and regulations and is hereby authorized to engage in the activity as indicated below.

Issued under the authority of the Illinois Department of Public Health

EXPIRATION 09/30/2023	CATEGORY 6A	055-008908
------------------------------	--------------------	-------------------

**CALUMET CITY PLBG & HTG CO INC
PLUMBING CONTRACTOR
REGISTRATION**

CALUMET CITY PLBG & HTG CO INC
281 River Oaks Drive
Calumet City IL 60409

MICHAEL GIGLIO

07 Cook

The face of this license has a colored background. Printed by Authority of the State of Illinois • P.O. #EH-21-044

OPERATING HISTORY

281 River Oaks Drive
Calumet City, IL 60409



(708) 868-0074 Office
ccp1967.com website

Completed Water Meter Replacements Through 10-11-22

Line No	Completion Year	Village / City Water Purveyor	Type of Installation	Manufacturer	Meter Count
1	1998	South Holland	Residential	ABB	2,500
2	1999	Robbins	Meter Vaults / Residential	Badger	1,025
3	2001	Willowbrook	Residential / Commercial	Badger / Hexagram	1,600
4	2001	Leyden Township	Residential / Commercial	Badger / Hexagram	3,000
5	2003	Elmwood Park	Residential / Commercial	Badger / Hexagram	6,170
6	2003	Bradley	Residential / Commercial	Sensus	260
7	2004	River Grove	Residential / Commercial	Badger / Hexagram	2,220
8	2005	Calumet Park	Residential / Commercial	Badger / Orion	1,580
9	2006	Arlington Heights	Residential / Commercial	Hersey / Itron	17,000
10	2009	Crete	Residential	S/S Inspection	2,325
11	2012	Midlothian	Residential / Commercial	Badger / Orion	3,700
12	2012	Tinley Park	Residential	Elster	800
13	2012	Aqua Illinois / Kankakee	Residential / Commercial	Sensus	3,000
14	2015	Willowbrook	Residential / Commercial	Aclara	1,600
15	2015	Elmwood Park	Residential / Commercial	Aclara	4,980
16	2015	Chicago Heights	Large Diameter Commercial	Sensus	840
17	2015	Country Club Hills	Residential / Commercial	Sensus	3,500
18	2016	Indian Head Park	Residential / Commercial	Badger / Itron	950
19	2016	Oak Forest	Residential / Commercial	Sensus	8,950
20	2017	Calumet City	Residential / Commercial	Sensus	9,200
21	2017	Glenbrook Sanitary District	Meter Vaults / Residential	Badger	350
22	2017	Joliet	Large Diameter Commercial	Sensus	18
23	2018	Harvey	Large Diameter Commercial	Sensus	64
24	2018	Lansing	Residential / Commercial	Sensus	8,990
25	2018	Highland Hills Sanitary District	Residential / Commercial	Badger	341
26	2018	Richton Park	Residential / Commercial	Sensus	3,350
27	2018	Joliet	Large Diameter Commercial	Sensus	33
28	2018	River Grove	Large Diameter Commercial	Badger	75
29	2019	Harvey	Residential / Commercial	Sensus	245
30	2019	Joliet	Large Diameter Commercial	Sensus	52
31	2019	East Chicago Indiana	Residential / Commercial	Master Meter	4,451
32	2019	West Suburban Water Commission	Large Diameter Commercial	Sensus	5
33	2019	Inspire Communities - Weather Stone Lakes	Residential Mobil Homes	Sensus	50
34	2019	Ely's Mobil Home communities	Residential Mobil Homes	Neptune	40
35	2019	River Grove	Large Diameter Commercial	Badger	133
36	2020	Burnham	Residential / Commercial	Sensus	1,172
37	2020	Phoenix	Meter Vaults / Residential	Badger	676
38	2020	Joliet	Large Diameter Commercial	Sensus	76
39	2020	Richton Park	Residential - Sample Test Meters	Sensus	66
40	2020	East Chicago Indiana	Residential / Commercial	Master Meter	34
41	2020	River forest	Large Diameter Commercial	Micrometer	2
42	2020	Naperville	Residential / Commercial	Sensus	903
43	2021	Joliet (2021 Commercial)	Large Diameter Commercial	Sensus	128
44	2021	Joliet (2021 residential) (Phase 1 & 2)	Residential	Sensus	462
45	2021	Summit	Residential / Commercial	Sensus	2,464

46	2021	East Chicago	Residential / Commercial	Master Meter	75
47	2021	Midlothian	Residential	Badger Beacon	333
48	2021	Naperville	Residential / Commercial	Sensus	147
49	2021	Country Club Hills	Residential / Commercial	Sensus	1,116
50	2021	East Hazel Crest (6-20-22)	Residential	Sensus	522
51	2021	Calumet Park	Commercial	Badger	11
52	2021	River Grove	Residential / Commercial	Badger	2,355
53	2021	Joliet Residential meters Phase 3	Residential	Sensus	210
54	2021	Joliet Large Diameter District Meters	Commercial Insertion Meters	Micrometer	2
55	2021	Robbins - Chicago Meter Vault	Commercial	Badger	2
56	2021	Acadia Realty - Merrillville Plaza	Commercial - Sub-Metering	Next Century	29
57	2022	Village of Oak Park (10-11-22)	Residential/ Commercial	Neptune	7,979
58	2022	Oak Forest Test Meters (6-22-22)	Residential/ Commercial	Sensus	108
59	2022	City of Hammond - Large District Meters	Large Diameter Commercial	Badger	4
60	2022	Joliet (2022 Commercial) (6-20-22)	Large Diameter Commercial	Sensus	14
61	2022	Justice Willow Springs Water Commission (10-11-22)	Residential / Commercial	Sensus	3,422
62	2022	DuPage County (Multiple Towns) (10-11-22)	Residential / Commercial	Sensus	3,288
63	2022	Darien (10-11-22)	Residential / Commercial	Sensus	2,193
				Total Installed	121,190

October 19, 2022

Calumet City Emergency Response time

Calumet City Plumbing is a 3 Generation Plumbing Company Serving the Chicagoland (6 County Area) & Northwest Indiana market in the Industrial, Commercial and Municipal Meter Replacement, Plumbing & Sewer Services for over 55 years. Our location in Calumet City is in close proximity to I-90/I-94, I-80/I-294, I-394 and I-57 makes it convenient to perform emergency service in a vast area. We have employees that take service vehicles home strategically placed around the Chicago and Northwest Indiana area that allow us to be on site quickly 24 hours - 7 days a week to diagnose & make emergency repairs. Our arsenal of equipment can be viewed on our website at WWW.CCP1967.COM

CCP has longevity with our employees given The Company years of experience in a vast array of plumbing, Water Meter and sewer related replacement and repairs.

Our Water Meter data collection and disbursement system allows us to process, store and distribute Municipal data that is compatible with all billing systems. Files can be converted into any format for Village entry. We are confident in our team and system that our data files will have a smooth transition in to the Village of Orland Park's Innoprise software.

QUALIFICATIONS

Village of Orland Park – RFP 22-062 – Water Meter Replacement Program Installation**Calumet City Plumbing – Comparable Project Experience References:**

City of Joliet
Jonathan C. Hall
Capital Program Engineer
815-724-4255 – Office
815-405-1695 – Cell
jhall@joliet.gov
116 N Chicago Street
Joliet IL, 60432

City of East Chicago
Winna Guzman
Director of Water Operation
219-391-8469 – Office
219-391-8499 – Cell
wguzman@eastchicago.com
400 East Chicago Ave
East Chicago, IN 46312

City of Calumet City
Gerry Surufka
Water Operator
708-891-8126 – Office
708-417-2233 – Cell
gsurufka@calumetcity.org
1701 Dolton Road
Calumet City, IL 60409

Justice-Willow Springs Water Commission
Colleen H. Kelly
Executive Director
708-458-7010 – Office
708-458-7017 Cell
ckelly@jswsc.org
7000 South Archer Road
Justice, IL 60458

Village of Lansing
Dan Podgorski
Village Administrator
708-895-7202 – Office
708-473-1627 – Cell
dpodgorski@villageoflansing.org
3141 Ridge Road
Lansing, IL 60438

Village of Richton Park
Michael Wegrzyn
Public Works Director
708-481-8950 – Office
708-774-4166 – Cell
mwegrzyn@richtonpark.org
4455 Sulk Trail
Richton Park, IL 60471

County of DuPage
Sean Reese
Operations manager – Department of Public Works
630-985-7400 – Office
630-864-7079 – Cell
Sean.reese@dupage.org
7900 S. Rout 53
Woodridge, IL 60517



September 23, 2022

RE: Calumet City Plumbing Reference Letter

To Whom It May Concern:

Calumet City Plumbing has remained under contract with the City of Joliet to provide a wide variety of meter services since 2019. They are currently under contract to replace over 5,000 meters, with an optional extension for an additional 5,000 meters.

Calumet City Plumbing has shown their commitment to the municipal metering industry by maintaining an extensive fleet of specialized equipment to handle the most complex, large meter projects. At the same time, they provide individual residential customers with the same high level of customer service for the smallest meter. The company has developed an efficient scheduling system for meter projects, providing excellent service to the customer and relieving the City of time-consuming scheduling tasks. When emergency work is required, the response time and result is always excellent.

We are very appreciative of the high quality of plumbing and specialized meter work provided by Calumet City Plumbing. The City relies heavily on them as a key partner in our ongoing efforts to provide excellent, cost-effective service to our customers.

Sincerely,

Jonathan C. Hall, P.E.
Capital Program Engineer



East Chicago Water Department

400 E CHICAGO AVENUE • EAST CHICAGO, IN • 46312

PHONE: 219.391.8469 • FAX: 219.391.8499

OFFICE HOURS: 8:30AM-4:30PM

WWW.EASTCHICAGO.COM

Honorable Anthony Copeland, Mayor

Winna G. Guzman, Director
wguzman@eastchicago.com

June 17, 2022

To Whom It May Concern:

I am writing this letter on behalf of Calumet City Plumbing Co., Inc., where the East Chicago Water Department has had the pleasure of working closely with Mr. Michael Giglio and the Calumet City Plumbing Co., Inc. staff relating to various water distribution improvements and maintenance projects.

The various projects include the replacement of water meters City-wide, replacement of lead service water lines and meter pit assemblies, replacing fire hydrant fixtures and valves, as well as assisting the City on maintaining small-large sized water mains on emergency basis throughout the past four (4) years. They have worked with the Water Department staff and presented various ideas and solutions that have been effective in completing several major projects, including detailed computer data and record keeping. They have also displayed professionalism with our City's residents in being responsive and attentive to communications, scheduling, concerns or issues. Because of their professionalism, expertise and knowledge, they continue to perform work as directed by our utility to assist the City in maintaining its complex distribution system.

Mr. Giglio and his team of staff are seasoned and skilled individuals and based on my experience in working with them, I can unreservedly state that they are well versed and have the ability to perform the various plumbing and distribution related type work as mentioned above. Should you have any questions or need additional information, please feel free to contact me.

Sincerely,

Winna Guzman



220 S. Westgate Carol Stream IL. 60188

Village of Bellwood
3200 Washington Blvd
Bellwood, IL 60104

June 17, 2021

RE: Bid Number: 2021-07-06 Water Meter Replacement Program

Attn: Procurement Services

Calumet City Plumbing is a qualified Advanced Meter Infrastructure (AMI) installation services company providing AMI compatible water meters. Calumet City Plumbing is a professional installation company capable of deploying AMI compatible water meters. Calumet City Plumbing has a well trained staff and excellent project management team. We, at Core & Main, trust Calumet City with deploying our AMI compatible products. Our experience working with them have been favorable and would recommend their services to anyone needing similar services.

Our experience with them include projects in Calumet City, Oak Forest, Richton Park, Lansing, Burnham, and currently in contract negotiations with many other utilities. We believe you would have favorable responses from all of these utilities utilizing their services.

Should you need to discuss anything further, you can contact me at any time.

Sincerely,

Jerry Plotke
Meter Systems Manager
jerry.plotke@coreandmain.com
708-774-8024

VILLAGE OF LANSING

Patricia L. Eidam
Mayor

Gary Richardson
Director of Public Works



Public Works

Patricia L.
Eidam
Mayor

Vivian Payne
Village Clerk

Saad Abbasy
Trustee

Mike Fish
Trustee

Maureen
Grady-
Perovich
Trustee

Brian Hardy
Trustee

Mike Manno
Trustee

Jerry
Zeldenrust
Trustee

January 10, 2020

Mr. Michael Giglio
President
Calumet City Plumbing Co., Inc.
281 River Oaks Drive
Calumet City, IL 60409

Re: Village of Lansing Water Meter Replacement Project

Dear Mr. Giglio-

I would like to take this opportunity to thank you & your Staff for the work done on our Water Meter Replacement Project. While we had been familiar with your Plumbing & Underground Repair work, we were also impressed with our Meter Project.

Your Staff from top to bottom were responsive, professional, & attentive to the needs of our residents throughout the Project. It is not the fact that issues will arise, but rather how they are handled when they do. We appreciate all of your Team's efforts.

Once again, thank you.

Sincerely,

Gary Richardson

Gary Richardson
Director of Public Works



December 14, 2018

Mr. Michael Giglio
President Calumet City Plumbing Co., Inc.
281 River Oaks Drive
Calumet City, IL 60409

Re: Richton Park Water Meter Replacement Project

Dear Mr. Giglio-

Thank you for a job well done! From start to finish Calumet City Plumbing did what you said you would. The Project was completed on time & budget. When issues arose, they were handled quickly & efficiently not only by your installers, but by your office staff as well.

As you know, we were cautious in sending any outside employees into our residents' homes. Our residents were treated with respect & courtesy throughout the Project.

Once again, thank you.

Sincerely,

A handwritten signature in black ink that reads "Regan Stockstell".

Regan Stockstell
Village Manager



**DUPAGE
COUNTY**

Wastewater

Water

Drainage

Permitting

PUBLIC WORKS DEPARTMENT

630-407-6800
Fax: 630-407-6701
publicworks@ec.dupageco.org

www.dupageco.org/publicworks

October 15, 2018

Mr. Michael Giglio
President
Calumet City Plumbing Co., Inc.
281 River Oaks Drive
Calumet City, IL 60409

Re: Highland Hills Water Meter Replacement Project

Dear Mr. Giglio-

Thanks to you & your entire staff. While the Project was smaller in nature, you would never know it from the manner in which Calumet City Plumbing handled the job. From our Pre-Con Meeting to our final install, you kept us ahead of the game.

Your Project Managers were hands on, skilled, & quick to respond. The job was completed on schedule, on budget & handled with professionalism throughout. We appreciate the polite & courteous interaction with our residents.

Once again, thank you.

Sincerely,

Sean Reese
Manager of Public Works Operations
DuPage County Public Works

OFFICE OF THE MAYOR

CALUMET CITY



MICHELLE MARKIEWICZ QUALKINBUSH

"AN ILLINOIS CERTIFIED CITY"

March 19, 2018

RE: Calumet City Plumbing-Municipal Wide Water Meter Replacement Project

To Whom It May Concern:

The City of Calumet City contracted with Johnson Controls in 2017 to upgrade our Water Metering Infrastructure. We were excited to learn that our own, local plumbing contractor, Calumet City Plumbing would be the Installer. We are well versed in many of their services.

The Project began in earnest in April of 2017 and was substantially completed last month. 9,200 water meters were replaced in seven months, two months ahead of schedule.

The service oriented staff-Installers, Field Foreman, Project Managers and appointment schedulers each did their part for a successful Project. Although there were a handful of difficulties as would be expected to accompany a Project of this scope, the staff resolved them promptly and to the complete satisfaction of our residents.

I am very pleased with the work completed by Calumet City Plumbing and I would highly recommend them for any Water Meter Infrastructure Project.

Sincerely,



Michelle Markiewicz Qualkinbush
Mayor

MMQ:rb

cc: file

15440 CENTRAL AVENUE
OAK FOREST IL 60452-2104



TELEPHONE: 708-535-4090
FAX: 708-687-2028

ALL GOOD THINGS CLOSE TO HOME

www.LivingOakForest.com www.Oak-Forest.org

March 1, 2017

RE: Calumet City Plumbing & Water Meter Installations

To Whom It May Concern:

In 2016 the City of Oak Forest undertook a city-wide water meter change-out program to upgrade our meter system to Sensus AMI radio read infrastructure. Calumet City Plumbing was secured by our performance contractor, Johnson Controls Inc., as the water meter installation contractor to change-out water meters ranging from ¾" up to six inch. Work began January 12, 2016 and was substantially completed in nine months with over 8,110 water meters installed by September 22, 2016.

Calumet City Plumbing committed dedicated resources to our project in the form of up to 12 meter installation technicians at peak work load. These field crews were supported by a project foreman working in the field, a project manager in the office, and a dedicated office support team that promptly addressed calls and concerns from both our residents and City staff.

I am very pleased with the work completed by the Calumet City Plumbing team and would not hesitate to call on them again to tackle another project for the City.

Please feel free to contact me with any questions about our meter change-out project.

Sincerely,

Richard Rinchich
Director of Public Works

UNDERSTANDING OF THE VILLAGE'S METER CONVERSION PROCESS

The Village of Orland Park
Proposed Water Meter Replacement Plan
October 19, 2022

Calumet City Plumbing (CCP) is pleased to present our proposed Methodology for scheduling, installation, and data management of the 2023-2024 Water Meter infrastructure upgrade for The Village of Orland Park (VOP). All water meters, transmitters, touch pads, wire and meter gaskets are to be supplied by the owner. Labor, equipment, appointment scheduling and data collection software are to be supplied by Calumet City Plumbing.

The Meter Replacement System will consist of the following:

Calumet City Plumbing to install water meters and transmitters (where needed). The majority of the interior meter replacements have the transmitters mounted on the outside of the building. All Pit meter replacements will have the transmitters mounted on the meter vault lid.

Village of Orland Park supplied Meters and support material will be available to CCP to have 24-hour access to the meter inventory and or old meter storage facility.

Meter Material to be supplied by the Village:

1. Meters 5/8" to 1" will be Sensus Iperl meters with touch-couple Flex Net transmitters.
2. Meters 1-1/2" to 4" will be Sensus Omni+ Meters with touch-couple Flex Net transmitters.
3. Meter gaskets, touch pads.
4. All Meters to be activated and/or programed by CCP using The Village of Orland Park Field Logic Configuration File (Provided by Core & Main).

Our Water Meter Installation program and procedures will provide The Village with quality installation performed by experienced licensed plumbers. Our plumbers and staff have passed an extensive background check.

We provide Project Management and Planning for scheduling of all appointments, meter installation, real-time data collection and retrieval for the VOP during the project, water service line material type inventory, daily, weekly and monthly reporting, and data files that can be converted and directly imported into the Village billing system. They Physical import to be performed by the Village.

Throughout the project, CCP will provide a listing of any non-responsive accounts, inaccessible meters, meters with non-working service valves illegal connections before the meter or location at which meters cannot otherwise be replaced. CCP will work with VOP to solve, correct, and install all that can be completed during the duration of the contract. At the close of the project, CCP will provide VOP with a file containing all Data and photographs captured during the project.

The VOP will be required to provide a detailed data file by spreadsheet with the following information:

- Account number
- Old meter serial number & existing transmitter number.
- Route or section number (based on read routes or other)
- Location type distinguishing Inside Set Meter or Pit Meter
- Old meter information (serial number, register number, transmitter number)
- Owner information: Name, address, Phone number
- Service location: Name of resident, address, Phone number
- Any other distinguishing information that will be helpful to identify the meter and or location.

The Process: Once the VOP data file has been provided to CCP with all the Water Service locations, their owners, mailing addresses, size and type of the existing water meter, the data is downloaded into our system, the mailing process will begin.

General Mail Plan: A series of letters, post cards and door tag notifications will be provided for review and approval prior to solicitation of any appointments.

Inside Set Meters:

1. The VOP to mail a “Kickoff” or introduction letter to all the service addresses and owners.
2. Approximately 2 weeks later, CCP to mail approximately 500 Initial letters and adjust for future mailing based on appointments made.
3. To those who do not make and appointments, a reminder Post Card will be sent 7 calendar days after the initial letter.
4. If an appointment is not made after the initial letter and the post card, a second reminder Post card will be mailed to the owner and service address.
5. If no appointment is made at that point, CCP will perform a Door Tag and hand deliver a final notice / water suspension letter. This will give the resident 5 days to call and make an appointment. If no appointment has been made, this account will be turned over to VOP. The Village can choose to post their own notice or turn the water off.
6. CCP will make no further attempt to contact the owner(s). However, CCP will assist with installing the meters as directed by the Village until either completion or other resolution.

This mail process from CCP will take approximately (4) weeks in each section. This process repeats itself until all new accounts have been notified according to the contract.

Pit Meters:

1. VOP to mail a “Kickoff” or introduction letter to all the service addresses and owners.
2. Approximately 2 weeks later, CCP to mail a Pit Meter letter based on the section of the Village that is being worked in. An appointment will only be necessary if the resident has

a locked gate or fence around the meter pit, or if they want to be home during the replacement. Otherwise, CCP will change the meter and leave a note on the door as to the date and time it was replaced.

Appointment Scheduling:

CCP will team up with M. E. Simpson for its scheduling of appointments, data collection and housing during the project.

Water customers will have the option of scheduling their appointment online to streamline the process or call our operator at (888) 252-1521. Online scheduling is fast and easy. To access the scheduling system simply go to www.ccp1967.com, and select the "Meter Appointment" blue tab at the top of the page, select The Village of Orland Park and follow the prompts.

Installation times:

We offer several convenient time blocks. Included in our bid are the following "typical" time blocks:

8:00 AM to 6:00 PM Monday through Thursday (**NO** Friday appointments).
Time blocks: 8:00 to 12:00, 12:00 to 4:00 and 4:00 to 6:00

8:00 AM to 4:00 PM Saturday (**NO** Sunday Appointments)
Time blocks: 8:00 to 12:00 and 12:00 to 4:00

Note: For water critical accounts, work can be scheduled other times. Our Project management team will perform a site survey and work this the resident or business owner to replace the meter at a convenient time.

Data Collection / Retrieval & Reporting:

CCP installers use iPad or smart phones to verify the old meter data & collect the new meter data. Backup photos for all facets of our installation process will be taken.

Included in our data package, (1) Water Department Representative will have access to our system and will be able to monitor the daily schedule, installations as they are entered, and daily totals and reports all in real time. This access will be available during the entire time the contract is open. Once closed, a file will be presented with all the data and photos from the project. Custom report will be created so the new installation information can be uploaded into the municipal billing system. Uploading or importing the data to be performed by the Village.

Included in the Proposal:

1. CCP will provide labor and material to remove and replace the existing water meters as directed. Meters are to be the same Lay Length as the existing meters (Drop In's), with no additional re-piping to complete the installation.
2. All Inside Set meters will have the Transmitter mounted outside the structure. Any exterior mounted transmitter will be installed using existing wire. Additional cost will apply for running new wire if required.
3. All Pit meter transmitters will be mounted on the existing meter lid.

4. Four attempts will be made to solicit an appointment as stated above. Once all four (4) are completed, CCP will make no further attempt to schedule. We will however assist in the installation of any and all water meters to assist the Village (within the parameters of this proposal).
5. All New and Old water meters are to be staged and stored by VOP. Old meters will be labeled with the date and address they were removed from.
6. Back up Photos: CCP will take pictures of the following:
 - a. Old meter serial number
 - b. Old meter read
 - c. Service Line Material type
 - d. General meter area
 - e. New meter serial number & transmitter number
 - f. New meter read
 - g. Copy of the CCP handwritten meter ticket with homeowner signature

Exclusions/Additional Costs (See Attached Rates):

1. Installation/replacement of meters with different lay lengths or flanged ends vs. threaded tail piece ends.
2. Piping in poor conditions – existing conditions.
3. Freezing an existing service line to replace a meter.
4. Cutting in service valves or replacing existing non-working valves.
5. Replacement of Meter vaults, frames and covers.
6. Replacement or repair of any B-box's.
7. Final restoration in non-hardscape or landscaping area.
8. Final restoration in hardscape areas (CCP will install Temporary cold patch to grade) where required.

Warranty:

Meters, transmitters and support material are to be supplied by VOP. As such, CCP is unable to provide any warranty on any materials purchased by VOP. These materials will be subject to the Manufacturer warranty at the time of purchase.

CCP to provide full one (1) year labor and material warranty on installation and any CCP provided materials.

November 19, 2022

Water Customer
XXXXXXXXXX
City, State, Zip Code

Your Account Key# (XXXXXX)

Dear Water Customer:

It's your turn to receive a new water meter for your property at XXXXXX in XXXXX. In an overall effort to modernize and better serve our residents & businesses, the Village of Orland Park has implemented a water meter replacement program. Meters will be replaced based on age. Your meter is included and will be replaced at this time.

The Village of Orland Park will pay the cost of the new meter and the installation.

Water customers will not be billed for the new meters.

To avoid possible Water Service Interruption, please schedule your appointment right away.

Flexible Timeslots available:

Monday through Thursday from 8:00am to 12(noon), 12(noon) to 4:00pm and 4:00pm to 6:00pm
Saturday from 8:00am to 4:00pm. An adult age 18 or older is required to be onsite during the replacement.

Please schedule on-line at CCP1967.com Or call (888) 252-1521

Upon receipt of this letter, residents & businesses are requested to schedule an appointment online with our installing contractor Calumet City Plumbing and their scheduling Management Company, M.E. Simpson at CCP1967.com click on the “Water Meter Appointment” Link, click on “Schedule an Appointment”, click the Bellwood tab, follow the instructions and then select your desired time slot), OR you can also call them (Toll Free) 1-888-252-1521, Scheduling personnel are available Monday through Friday 8:00am to 3:30pm. You can leave a message with your information after 3:30pm and scheduling personnel will return your call.

As the meter installer from Calumet City Plumbing will need to shut the water off for the meter replacement, it is necessary for residents to have internal shutoff valves in proper working order. If you do not have a working internal valve (street side of the meter), or are unsure if it is working, please inform M.E. Simpson of this fact when you make your appointment, so that arrangements can be made to shut your service off at the street for the duration of the meter replacement. To assist in these efforts, please make sure that your water meter is easily accessible to the installer and that the individual present during the appointment must be at least 18 years old.

Each Installer has passed a background check with the Village of Orland Park and will present an identification badge to residents before entering the home. Do not admit anyone into your home that does not have a Village of Bellwood picture identification card.

If you have any Concerns, please contact the Village of Orland Park at 708-XXX-XXXX and your question will be directed to the appropriate staff member.

Please schedule an appointment with **M.E. Simpson Company** one of two ways:

1. ONLINE - www.ccp1967.com Enter Account Key: XXXXXX
2. CALL - (Toll Free) **1-888-252-1521**




Calumet City Plumbing

*** Excellence Since 1967 ***

We Don't Say "We Do It" Unless We've Done It.

[CONTACT / MORE INFORMATION](#)

[VIEW OUR SERVICES](#)

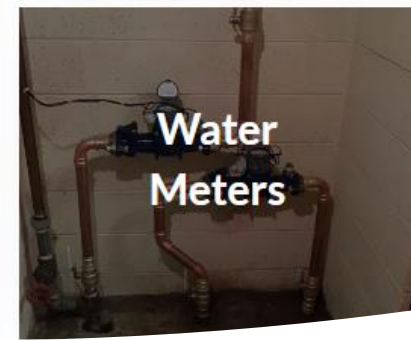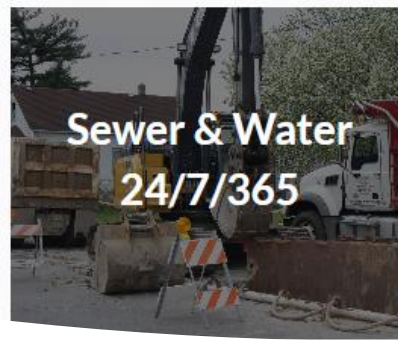

Calumet City Plumbing Utility Data Integration Methodology Client Access Information

- 
-
- 001. Grid Map Sample
 - 002. Client Dashboard
 - 003. Generated Mailer Report
 - 004. Turn-Over List
 - 005. Complete Accounts
 - 006. Upcoming Appointments
 - 007. Week View Scheduled Appointments
 - 008. Pre-Work Issues
 - 009. Add-On Charges
 - 010. Appointment Scheduling

001. Grid Map

CCP coordinates appointments with ease, each pin represents an address. It can be sorted by technician, date and time block.

DuPage County, IL: 2022 DuPage County Installs Return to QB

Filter

Status
Nothing selected

Assigned Tech
Nothing selected

Date
10/17/22 to 10/19/2022

Start/End
8:00 am - 12:00 pm

First Appt
No

Grid
Value to update: 1
Update

Keyboard shortcuts | Map data ©2022 Google | Terms of Use | Report a map error

002. Client Dashboard


Data package includes real time access to monitor daily schedules, installations and daily reports

Today's Appointments

Account Num	Project Name	Date	Start	End	Status (color)	Schedule Status (today)	Scope	Technician Team	Technician Phone
14508746	2022 DuPage County Installs	10-18-2022	8:00 am	12:00 pm	FIRST Visit Complete	Visit Complete	Meter (R)	Michael Szymanski (30)	(847) 915-1563
10100395	2022 DuPage County Installs	10-18-2022	8:00 am	12:00 pm	Visit Complete	Visit Complete	Meter (R)	Garrett Martinez (25)	(219) 741-7140
10100469	2022 DuPage County Installs	10-18-2022	12:00 pm	4:00 pm	Scheduled Assigned	Appt Today 7.4 hrs until block expires	Meter (R)	Garrett Martinez (25)	(219) 741-7140
10100332	2022 DuPage County Installs	10-18-2022	12:00 pm	4:00 pm	Scheduled Assigned	Appt Today 7.4 hrs until block expires	Meter (R)	Garrett Martinez (25)	(219) 741-7140
10100338	2022 DuPage County Installs	10-18-2022	4:00 pm	6:00 pm	Scheduled Assigned	Appt Today 5.4 hrs until block expires	Meter (R)	Garrett Martinez (25)	(219) 741-7140

Vacant / Skip Accounts

Account Number	Account Key	Customer Name	Service Address	Account Status	A Comments
=10009048"	33-2852	First Student	22W760 Poss Avenue		[U]-08-22 9:37 AM Ashley Ditchcreek] This is a deduct meter
=10009056"	33-1733	Extra Space Storage / Engie Insight	1N371 Highland Avenue		
=10009081"	33-2232	Falin Wang	1N577 Main Street		
=10009083"	33-2231	Mark Movagh	1N571 Main Street		
=10009087"	33-2228	Charles Mitchell	1N531 Main Street		
=10009098"	33-2225	Denise Keiper	1N459 Main Street		
=10009099"	33-2224	Adhikari Ganapati	1N455 Main Street		

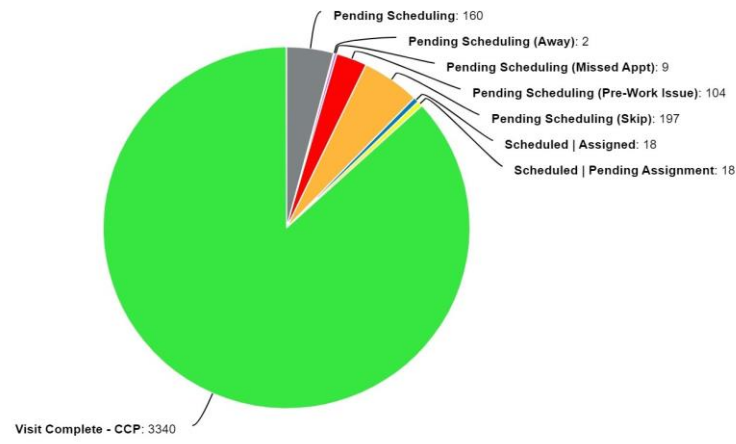

- Pending Scheduling
- Pending Scheduling (Away)
- Pending Scheduling (Missed Appt)
- Pending Scheduling (Pre-Work Issue)
- Pending Scheduling (Skip)
- Scheduled | Assigned
- Scheduled | Pending Assignment
- Visit Complete - CCP

003. Generated Mailer Report

CCP will mail three letters, including one door tag to each service address requesting to schedule an appointment. CCP will make every effort to accommodate the customers in scheduling and/or rescheduling of their appointment.

Project Name	Group Name	# of Accounts	# of Accounts - Letter	# of Accounts - 1st Postcard	# of Accounts - 2nd Postcard	# of Accounts - 3rd Postcard	# of Accounts - 4th Postcard	# of Accounts - Door-Knock List
2022 DuPage County Installs	Endpoint Only (North)	661	661	1	1	0	0	0
2022 DuPage County Installs	Meters (Lombard)	37	37	26	22	0	0	0
2022 DuPage County Installs	Endpoint Only (South)	365	365	0	0	0	0	0
2022 DuPage County Installs	Meters (Itasca)	250	249	180	112	0	0	0
2022 DuPage County Installs	Meters (Glen Ellyn)	397	397	282	158	0	0	0
2022 DuPage County Installs	Meters (North Naperville)	644	644	424	197	0	0	0
2022 DuPage County Installs	Meters (Darien)	692	692	499	233	0	0	0
2022 DuPage County Installs	Meters (Darien) 2	694	694	468	303	0	0	0
2022 DuPage County Installs	Meters (South Naperville)	108	108	74	50	0	0	21
TOT		3848	3847	1954	1076	0	0	21

004. Turn-Over List

Throughout the project, CCP will provide a listing of any non-responsive accounts, inaccessible meters, meters with non-working service valves or locations at which meters cannot otherwise be replaced. CCP will work with the City to solve, correct, and install all that can be completed during the duration of the contract.

Meter Installation : Accounts | DuPage County Turnover Listing

DuPage County Turnover Listing

Status (color)	Account Key	Acct #	Mailing Group #	Door Knock List #	Class	Billing	Address	Street	Turn Over List #	Cycle	A Comments	Appt/Install Date	Shut Off List #	Service Address 1	Service Address 2	Billing Address 1 (formula)	Billing Address 2 (formula)
Pending Scheduling	33-0022	= "14015828"	Meters (Lombard)	1		Garrett Muersch & Bingying Ye	18W780	14th Street	1					18W780 14th Street	Lombard, IL 60148		
Pending Scheduling	33-0033	= "14015832"	Meters (Lombard)	1		Amin Razzak	824	14th Street (E)	1					824 14th Street (E)	Lombard, IL 60148		
Pending Scheduling	33-0488	= "14508742"	Meters (Itasca)	2		Jason Phelps	5N315	Bunker Terrace	2					5N315 Bunker Terrace	Itasca, IL 60143		
Pending Scheduling	33-0491	= "14508738"	Meters (Itasca)	2		Angie & Greg McCulloch	5N340	Bunker Terrace	2					5N340 Bunker Terrace	Itasca, IL 60143		
Pending Scheduling	33-1304	= "14508689"	Meters (Itasca)	2		Edward Shoffner	5N376	Fairway Lane	2					5N376 Fairway Lane	Itasca, IL 60143		

005. Completed Accounts

Monthly progress report will be included with the invoice providing an overview of billable account activity.

Meter Installation : Accounts | DuPage County Completed Accounts

DuPage County Completed Accounts

Account Key	Appt/Install Date	Technician	Group Name	Customer Name	Contact Number	Service Address	Service City	Service Zip	Account Num	Old Meter Serial Number	Old Radio Number	Old / Final Meter Reading	Compound Read	Feet / Gallons	New Meter Size	New Serial Number	New Meter Reading
<i>(empty) (209 Account records)</i>																	
33-0565	09-29-2022		Endpoint Only (South)	Sameen Tariq and Zeeshan Ali		10S417 Carrington Circle	Burr Ridge	60527	-*17506270*	-*68818383*		-*0254494*		Gallons			
33-0566	09-29-2022	Martinez, Garrett	Endpoint Only (South)	American Homes 4 Rent	(810) 919-9032	10S418 Carrington Circle	Burr Ridge	60527	-*17506273*	-*68818385*		-*0597861*		Gallons			
33-0567	09-29-2022		Endpoint Only (South)	Jason Schlender		10S419 Carrington Circle	Burr Ridge	60527	-*17506269*	-*68924671*		-*0226683*		Gallons			
33-0569	09-29-2022		Endpoint Only (South)	Adnan Mehmood		10S421 Carrington Circle	Burr Ridge	60527	-*17506271*	-*68818386*		-*0450722*		Gallons			
33-0588	09-29-2022		Endpoint Only (South)	Peter Younan		10S440 Carrington Circle	Hinsdale	60527	-*17506277*	-*65295871*		-*0622793*		Gallons			
33-0592	09-29-2022		Endpoint Only (South)	Marwah Muhammed		10S444 Carrington Circle	Hinsdale	60527	-*17506279*	-*68924669*		-*0451958*		Gallons			

005. Upcoming Appointments

With the data access, the City will be able to view upcoming appointments.

Appointments > Upcoming Appts

▶ Reports & Charts

 New style
 






















 You made changes 

The next week's worth of appointments.


 Project Name (1)
 Status (color)
 Schedule Status (today)
 Scheduled Block - Date

42 appointments where Date is on or after ...

Project Name  Clear all

Appointment Status	Appointment Date	Time Block	First Appt of Day ↓	Service Address	Old Meter Size	Work Scope	MXU Replace or Reprogram	Technician Name	Notes	Account Num (export)	Account Key	Route	
	10-17-2022 - 11-19-2022								<input type="text"/>				
10-17-2022 (4 appointments)													
Mon (4 appointments)													
 	Visit Complete	10-17-2022	8:00 am - 12:00 pm	<input type="checkbox"/>	21W325 Tee Lane	3/4 in - Short	Meter Replacement	Replace	Michael Szymanski		"14508757"	33-3595	Itasca
 	Visit Complete	10-17-2022	12:00 pm - 4:00 pm	<input type="checkbox"/>	1N686 Park Boulevard	3/4 in - Short	Meter Replacement	Replace	Dan Hillock		"10009302"	33-2728	Glen El
 	Visit Complete	10-17-2022	12:00 pm - 4:00 pm	<input type="checkbox"/>	1N580 River (1440 River Rd.) Drive	3/4 in - Short	Meter Replacement	Replace	Dan Hillock		"10009366"	33-2981	Glen El
 	Visit Complete	10-17-2022	4:00 pm - 6:00 pm	<input type="checkbox"/>	136 Bonnie Brae Lane	1-1/2 in	Meter Replacement	Replace	Garrett Martinez	RL 8/27/22 found meter is a 22" spread with 2" flange couplings. Explained to the customer that I would need to see if I had all material available to repipe and	"19503507"	33-0441	Darien

007. Week View Scheduled Appointments

City will have access to view upcoming appointments

Appointments > Upcoming Appts
 ▶ Reports & Charts

New style [+ New Appointment](#)    You made changes 

The next week's worth of appointments.

Search records (1) Project Name Status (color) Schedule Status (today) Scheduled Block - Date (1)

1 - 200 of 396 appointments where Date is on or after ...

Scheduled Block - Date x 10-16-2022 - 10-22-2022 x Clear all

Appointment Status	Appointment Date ↑	Time Block	First Appt of Day ↓	Service Address	Old Meter Size	Work Scope	MXU Replace or Reprogram	Technician Name	Notes	Account Num (export)	Account Key	Route
<input type="text" value="Filter"/>	10-16-2022 - 10-22-2022	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>	<input type="text" value="Filter"/>
▼ 10-18-2022 (125 appointments)												
▼ Tue (125 appointments)												
Scheduled Assigned	10-18-2022	8:00 am - 12:00 pm	✓	609 Maple Lane	Not Provided	Meter Replacement		Dan Hillock	10/13: Homeowner requested to have the valve replaced and is aware of the additional cost.	= "21001788"	34-5634	223A
Scheduled Assigned	10-18-2022	8:00 am - 12:00 pm	✓	7516 Cass Avenue (S)	Not Provided	Meter Replacement		Agustin Avitia	Burrito Paradise location. Freestanding building on Cass Ave. Unit 33.	= "21002465"	34-2084	211A
Scheduled Assigned	10-18-2022	8:00 am - 12:00 pm	✓	338 Janet Avenue	5/8 x 3/4 in	Meter Replacement		Karl Jonas		= "21004987"	34-4963	239B
Scheduled Assigned	10-18-2022	8:00 am - 12:00 pm	✓	6900 Route 83	Not Provided	Meter Replacement		Jim Cobb	Located in the back room by the 3 compartment sink. They open at 5AM, so someone will be there for the first appointment.	= "21010445"	34-7011	241B

008. Pre-Work Issues

CCP's objective is to complete the installation on the 1st appointment, if CCP is unable to install the meter, we assign it as a pre-work and follow up and reschedule.

Meter Installation : Pre-Work Issues | [Pre-Work Issues Home](#)

Pre-Work Issues Home

Account Status	Appt / Install Date	Account Key	Account Number	Customer Name	Service Address	Work Scope	Old Meter Size	Issue Type	Issue Status	Issue Notes	Mail Group	Door Knock List #	Turn Over List #
Pending Scheduling (Pre-Work Issue)	07-11-2022	33-0047	14100012	York Center Park District Drink Fountain	16th Street, Knolls Park	Install Endpoint Only	1 in	Pit Meter	Open	7/11/2022 Pit Meter located right in front of Knolls Park sign. Badger meter with register head MXU# 17987644 (matches w/Go Canvas MXU) *No radio transmitter wire Meter is approximately 15" down and pit opening width approximately 12" CSSE will not be necessary -DH-33	Endpoint Only (North)		
Pending Scheduling (Pre-Work Issue)	07-11-2022	33-3010	14015774	Daniel and Leah Pedersen	679 Rochdale Circle	Meter Replacement	3/4 in - Short	Pit meter	Open	RL 7/11/22 meter is in pit out front.	Meters (Lombard)		
Pending Scheduling (Pre-Work Issue)	07-12-2022	33-0006	14015842	Ben and Patricia Shapera	18W740 13th Street	Meter Replacement	3/4 in - Short	Pit meter	Open	RL 7/12/22 meter is in pit in front of house. Looks like meter is an ipearl.	Meters (Lombard)		

009. Add-On Charges

Exclusions/Additional Costs: Ground clamps, wire, valve installation, re-piping, etc.

Meter Installation : Add-On Charges | [Add-on Charges Home](#)

Add-on Charges Home

Project Name	Appt/Install Date	Account Key	Account Num	Cycle	Service Address	Service Type	Charge Type	Quantity	Charge Notes
2022 DuPage County Installs	06-30-2022	33-1306			5N385 Fairway Lane, Itasca, IL 60143	Copper	Install ground clamps and wire	1	
2022 DuPage County Installs	07-07-2022	33-1308			5N408 Fairway Lane, Itasca, IL 60143	Copper	Install ground clamps and wire	1	
2022 DuPage County Installs	07-07-2022	33-2853			23W040 Poss Street, Glen Ellyn, IL 60137	Copper	Install ground clamps and wire		
2022 DuPage	07-07-2022	33-2851			22W760 Poss Avenue, Glen		Install ground		

010. Appointment Scheduling

Online scheduling is fast and easy. To access the scheduling system simply go to www.ccp1967.com select the “Water Meter Appointment” blue tab at the top of the page, on the next screen, select the “Schedule an Appointment”

📞 Emergency Service IL/IN: 708-868-0074

📅 Water Meter Appointment 📅 Water Service Line Appointment



HOME

ABOUT

SERVICES

MARKETS

EMERGENCIES

SAFETY

CAREERS

CONTACT

Water Meters

Schedule Water Meter Replacement:

SCHEDULE AN APPOINTMENT →

PROPOSED FEE

CCP

VOP Project Rate Sheet for Repairs - 10-19-22

LABOR	RATE	OT	DT				
Apprentice	\$ 110.00	\$ 135	\$ 153				
Foreman	\$ 135.00	\$ 170	\$ 195				
Laborer	\$ 120.00	\$ 153	\$ 173				
Operator	\$ 135.00	\$ 170	\$ 195				
Plumber	\$ 135.00	\$ 170	\$ 195				
Project Manager	\$ 135.00	\$ 170	\$ 195				
Equipment	Rate	UNIT					
Site Truck	\$ 38.00	PER HR.					
A/C Tow Behind	\$ 25.00	PER HR.					
P/U Truck 4x4	\$ 25.00	PER HR.			UNIT		
Mini Excavator	\$ 45.00	PER HR.	1"	STONE	TON	\$ 21.60	
Medium Excavator	\$ 55.00	PER HR.	3/4"	STONE	TON	\$ 16.80	
Large Excavator	\$ 65.00	PER HR.	N/A	COLD PATCH	TON	\$ 162.00	
Combination Backhoe	\$ 60.00	PER HR.	N/A	BLACK DIRT	C YRD	\$ 25.00	
EQ1802 Breaker BH	\$ 130.00	L.S.	N/A	SPOIL TO CCP	C YRD	\$ 25.00	
Bobcat	\$ 45.00	PER HR.	N/A	SPOIL OUT	C YRD		
	\$ -		N/A	CONCRETE	C YRD	\$ 135.00	
1 Ton Dump	\$ 38.00	PER HR.	N/A	CONCRETE DELIVERY	N/A	\$ 200.00	
Medium Trailer (Electric)	\$ 45.00	PER HR.					
Medium Dump (TR385)	\$ 43.00	PER HR.		Sewer Bricks	each	\$ 0.55	
6 Wheel Dump (Mack/211)	\$ 53.00	PER HR.		Sewer Blocks	each	\$ 8.00	
Tag Trailer	\$ 65.00	L.S.		80 lb. concrete	bag	\$ 15.00	
Comb. Jet/Vac Truck	\$ 160.00	PER HR.		spread Crete	bag	\$ 25.00	
Shore Box	\$ 65.00	L.S.					
Plate Compactor	\$ 125.00	L.S.		FREEZE KIT	LS	\$ 125.00	
TR 403 Camera Truck	\$ 55.00	PER HR.		300 MACHINE	LS	\$ 12.00	
Tow Behind Arrow Board	\$ 165.00	L.S.		CAMERA ONLY	LS	\$ 85.00	
Port a Drill	\$ 295.00	L.S.		GANTRY	LS	\$ 35.00	
CSEE	\$ 135.00	L.S.		HYDRO PUMP	LS	\$ 30.00	
Directional Drill Rig	\$ 595.00	L.S.		POUNDER/PUSHER	LS	\$ 25.00	
EZ Valve Trailer	\$ 495.00	L.S.		DESCALER EQUIP	LS	\$ 120.00	
Well Point Trailer	\$ 325.00	L.S.	19'	MAN LIFT	LS	\$ 245.00	
Tow-Behind Jetter	\$ 295.00	L.S.	26'	MAN LIFT	LS	\$ 345.00	
Shore Box (Large)	\$ 110.00	L.S.	NOTE: Any Material required for repairs will be charged at CCP cost Plus 10% mark-Up				
GAS JETTER	\$ 145.00	L.S.					
THAWING EQUIP.	\$ 125.00	L.S.					
Line Location Equipment	\$ 110.00	L.S.					
Smoke Test Equipment	\$ 135.00	L.S.					

SECTION 3 – PROPOSED SCHEDULE OF INSTALLATION WORK

10/18/2022

Calumet City Plumbing Proposed Schedule

Village of Orland Park Water Meter Replacement Program RFP 22-062



Task No	Task Name	Start	Duration	Finish	2020-2030																							
					2022			2023												2024								
					November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August		
10	Anticipated NTP	01/02/2023	1	01/02/2023																								
20	Preconstruction Meeting	11/21/2022	1	11/21/2022																								
30	Request/Receive Data for Review	11/21/2022	1	11/21/2022																								
40	ME Simpson Data Integration	11/21/2022	60	01/19/2023																								
50	Approval of General Mail Plan-Letters/Postcards	11/21/2022	30	12/20/2022																								
60	Background Checks	11/21/2022	30	12/20/2022																								
70	Website Set Up	12/21/2022	30	01/19/2023																								
80	QuickBase/Sensus Installer Process Overview	12/21/2022	45	02/03/2023																								
90	Village of Orland Park Kick Off Letter	01/09/2023	1	01/09/2023																								
100	CCP Initial Letter	01/23/2023	15	02/06/2023																								
110	*Installation Process	02/13/2023	540	08/05/2024																								
120	Post Card 1 (Repeats every 2 Weeks)	02/01/2023	501	06/15/2024																								
130	Post Card 2 (Repeats every 2 Weeks)	02/06/2023	503	06/22/2024																								
140	Turnover List (Repeats every 2 Weeks)	02/16/2023	510	07/09/2024																								
150	Project End Date for Regular Appointments	08/05/2024	1	08/05/2024																								
160	Close-Out Punchlist	07/15/2024	30	08/13/2024																								

*Note: Proposed 18 Month Completion Schedule can be adjusted to meet the Village of Orland Park's requirements from 1-2 years.

Calumet City Plumbing
Telephone 24/7: 708-868-0074

Project Manager: Rodney Tracy
Assist. P/M: Jeannette Salinas

Cell: 815-821-5893
